

US 70 Projects Update

April 18, 2019




NCDOT

DIVISION 4

**Corridor Upgrades
Feasibility Studies
Resurfacing**

TIP: W-5600

US 70 Johnston County

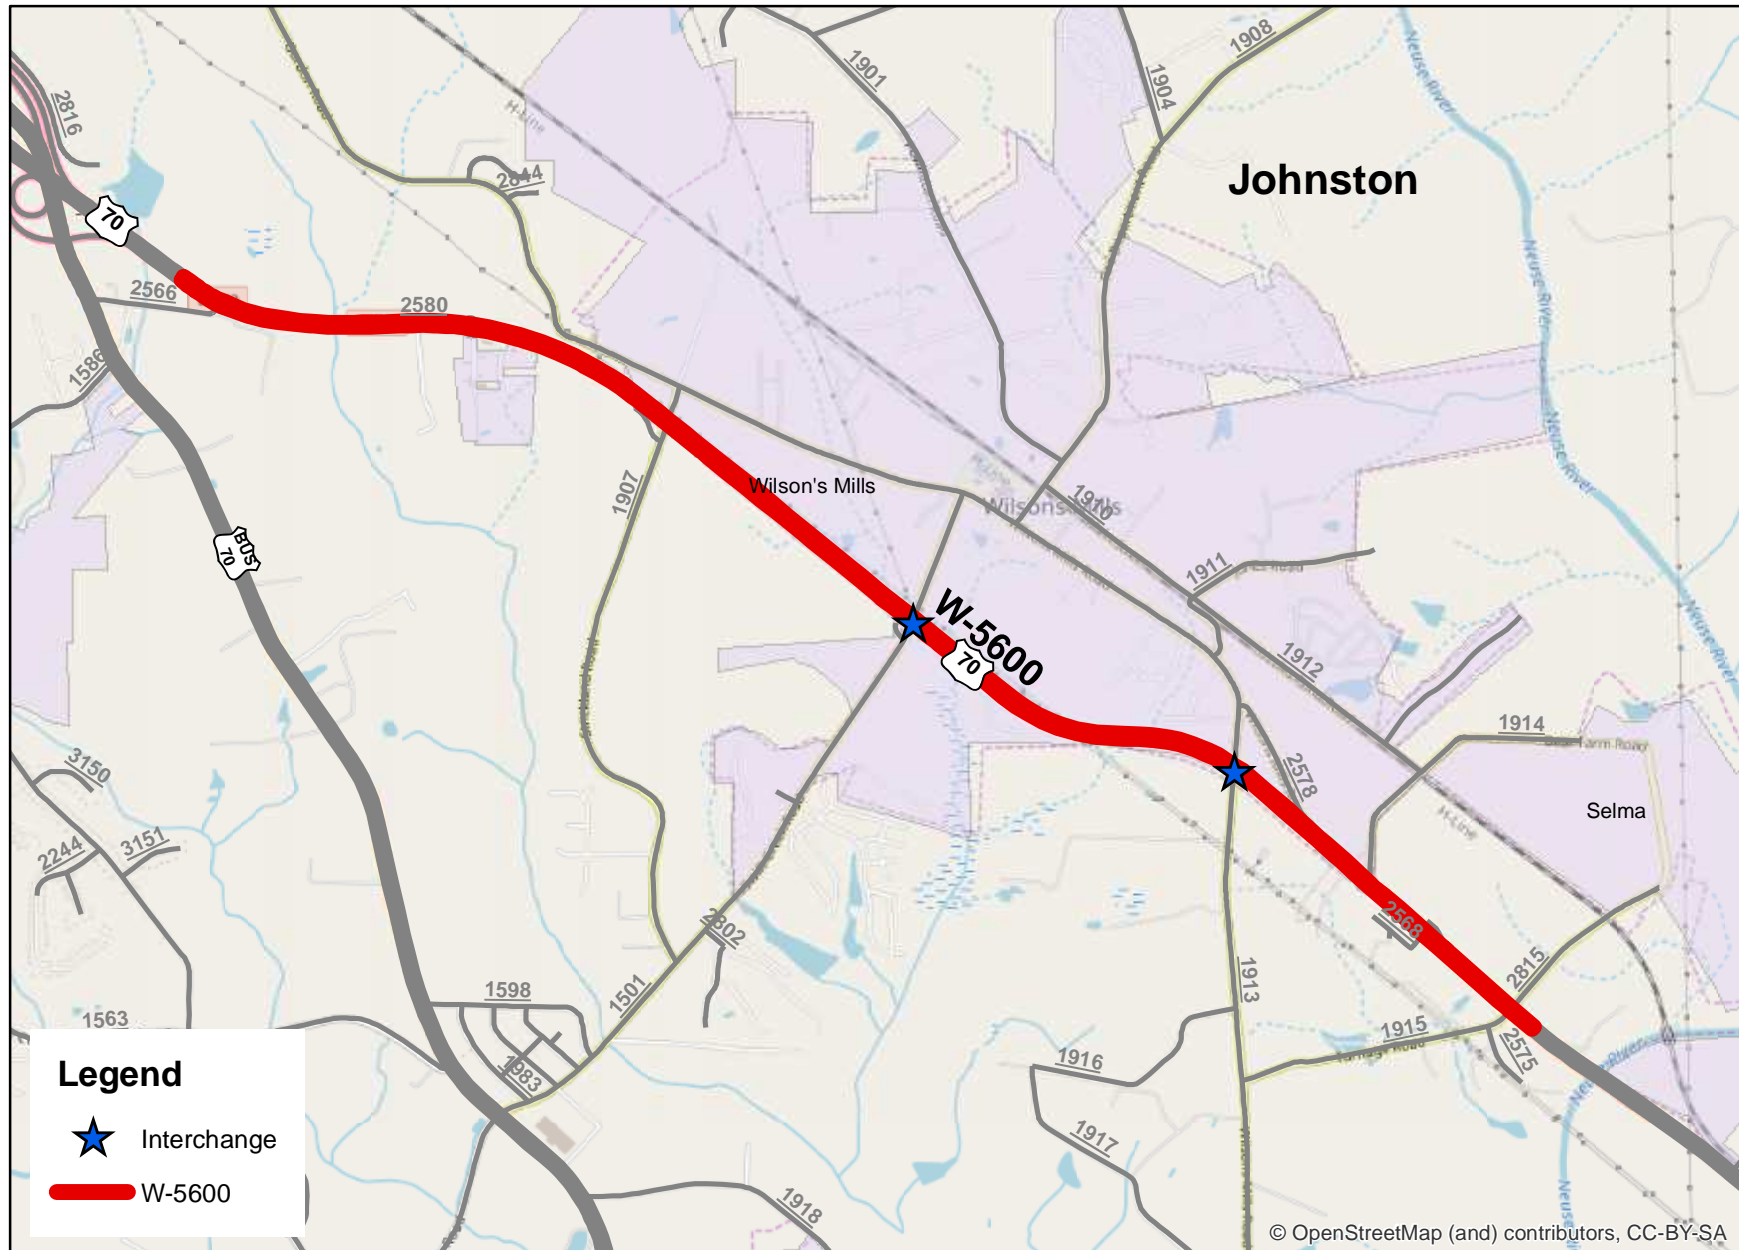

W-5600

US 70 Improvements near Wilson's Mills - Johnston County

Project Description:

Upgrade US 70 to Interstate standards from US 70 Business to Neuse River.

Funding Status:

Fully funded in 2018-2027 STIP.

Schedule:

- Project Scoping Meeting - July 2012
- Public Meeting - February 2016
- CE Approved - July 2016
- Right of Way Acquisition – March 2018
- Construction – Scheduled for January 2020

Activities Underway


- Right of way acquisition will be complete in June 2019
- Utility Relocations are being scheduled.
- 90% plans are complete.

Upcoming Actions

- Complete right of way acquisition.
- Begin Utility Relocation.
- Duke Transmission relocations
- Final plans.
- Project letting and award.

Project Manager: Matt Clarke, P.E., (252) 640-6400, wmclarke@ncdot.gov

TIP: R-5829
US 70 Wayne - Johnston Counties

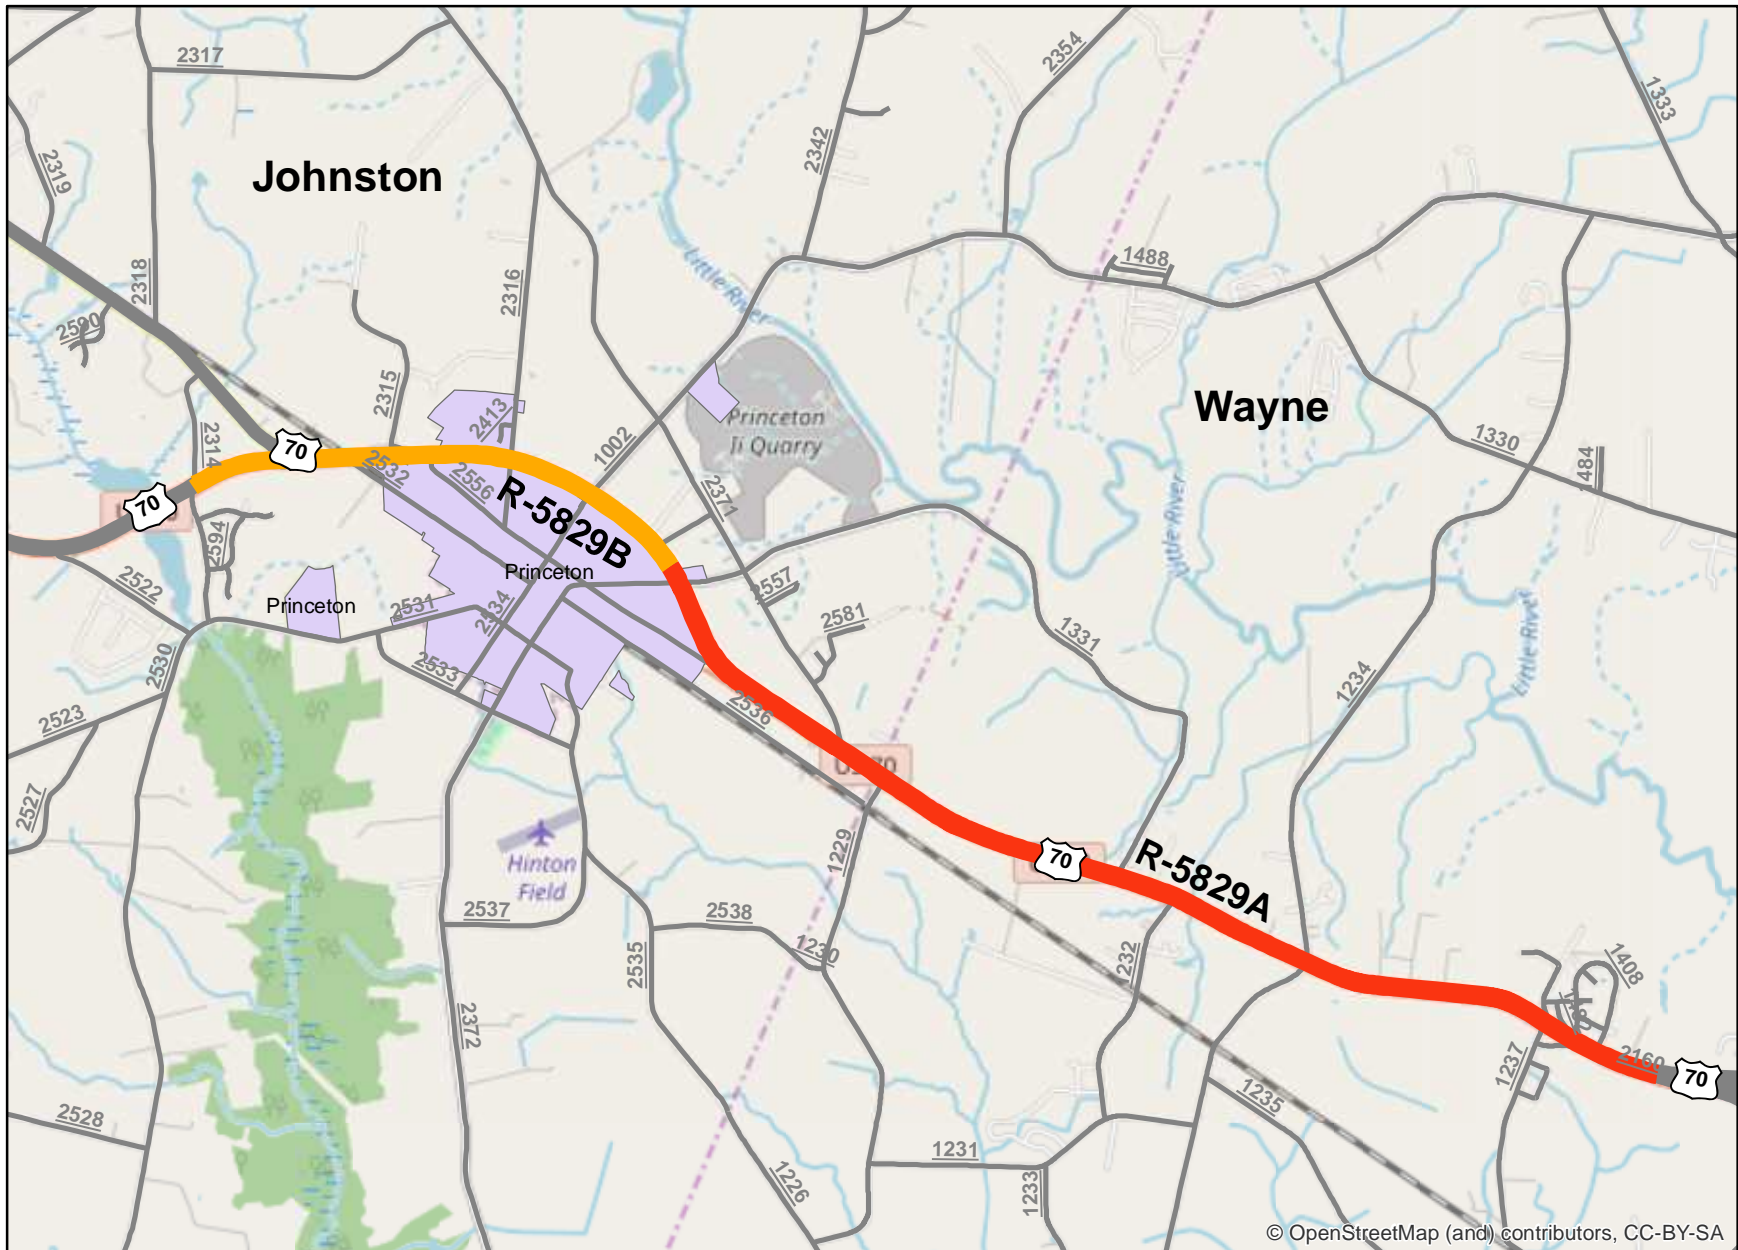

R-5829A & R-5829B

US 70 Improvements near Princeton - Johnston County

Project Description:

Upgrade US 70 to Interstate standards from US 70 Goldsboro Bypass to West of US 70A.

Funding Status:

Currently funded in 2018-2027 STIP.

Schedule:

- Traffic Forecast - May 2018
- Surveys Complete - December 2018
- Preferred Alternative Selected - October 2018
- Public Hearing - March 2019
- Environmental Document Approved - July 2019
- Design Bid Build Let* – R-5829A FY 2025

R-5829B FY 2028

Activities Underway

- Develop Public Meeting map.
- Complete Environmental Assessment.
- Noise Analysis.


Upcoming Actions

- Public Meeting - May 21
- Determine steps forward based on funding.
 - Design-Build letting
 - Final Plan Production
 - Right of Way acquisition

Project Manager: Matt Clarke, P.E., (252) 640-6400, wmclarke@ncdot.gov


***Project can be accelerated if funding is available.**

FS-1604A - US 70 Johnston County

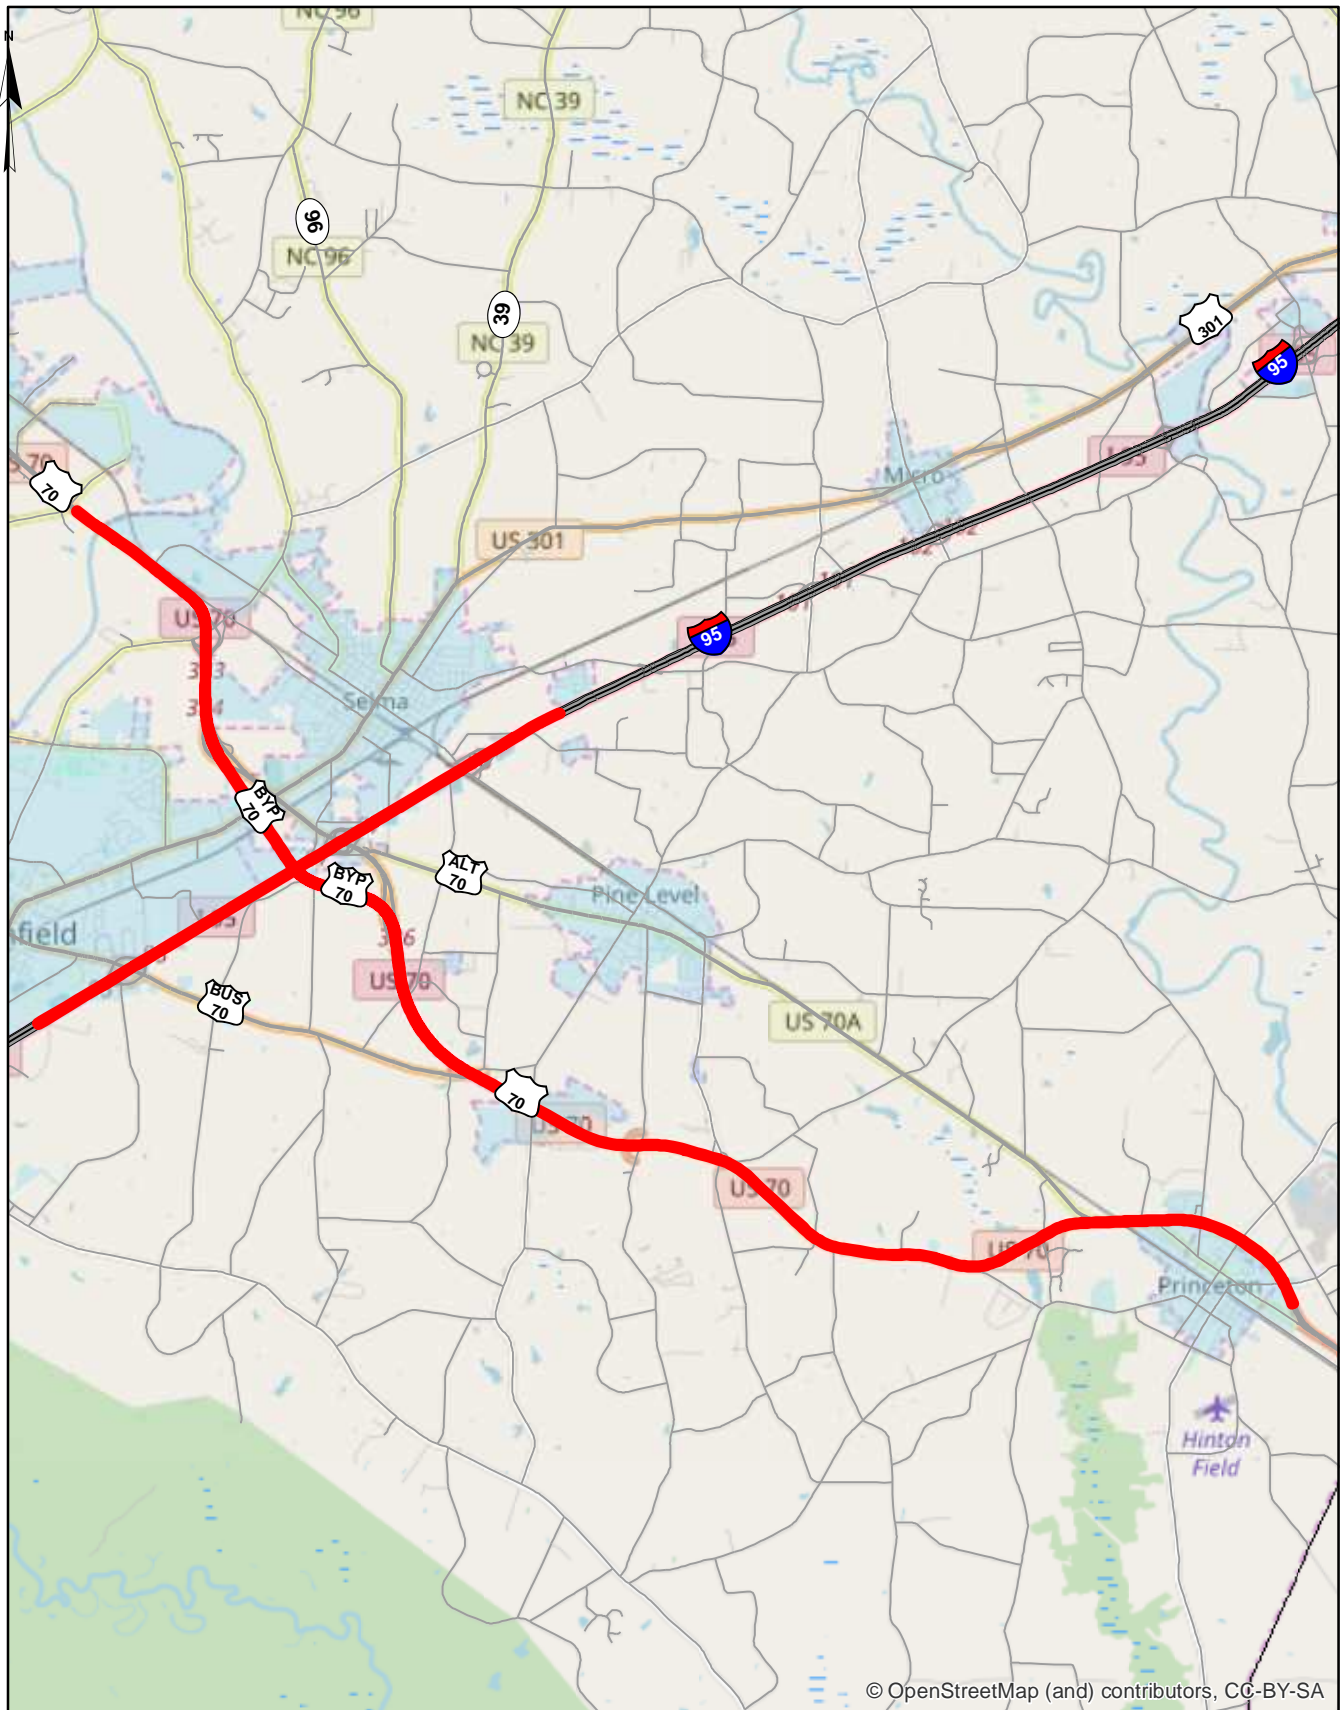


Feasibility Study for US 70 from SR 1003 (Buffalo Road) near Selma to SR 2372 (Edwards Road) in Princeton Completed Date: August 2018
Link: https://connect.ncdot.gov/projects/planning/FeasibilityStudiesDocuments/Feasibility-Study_1604A_Report_2018.pdf

C204032 - US 70 Johnston County Resurfacing

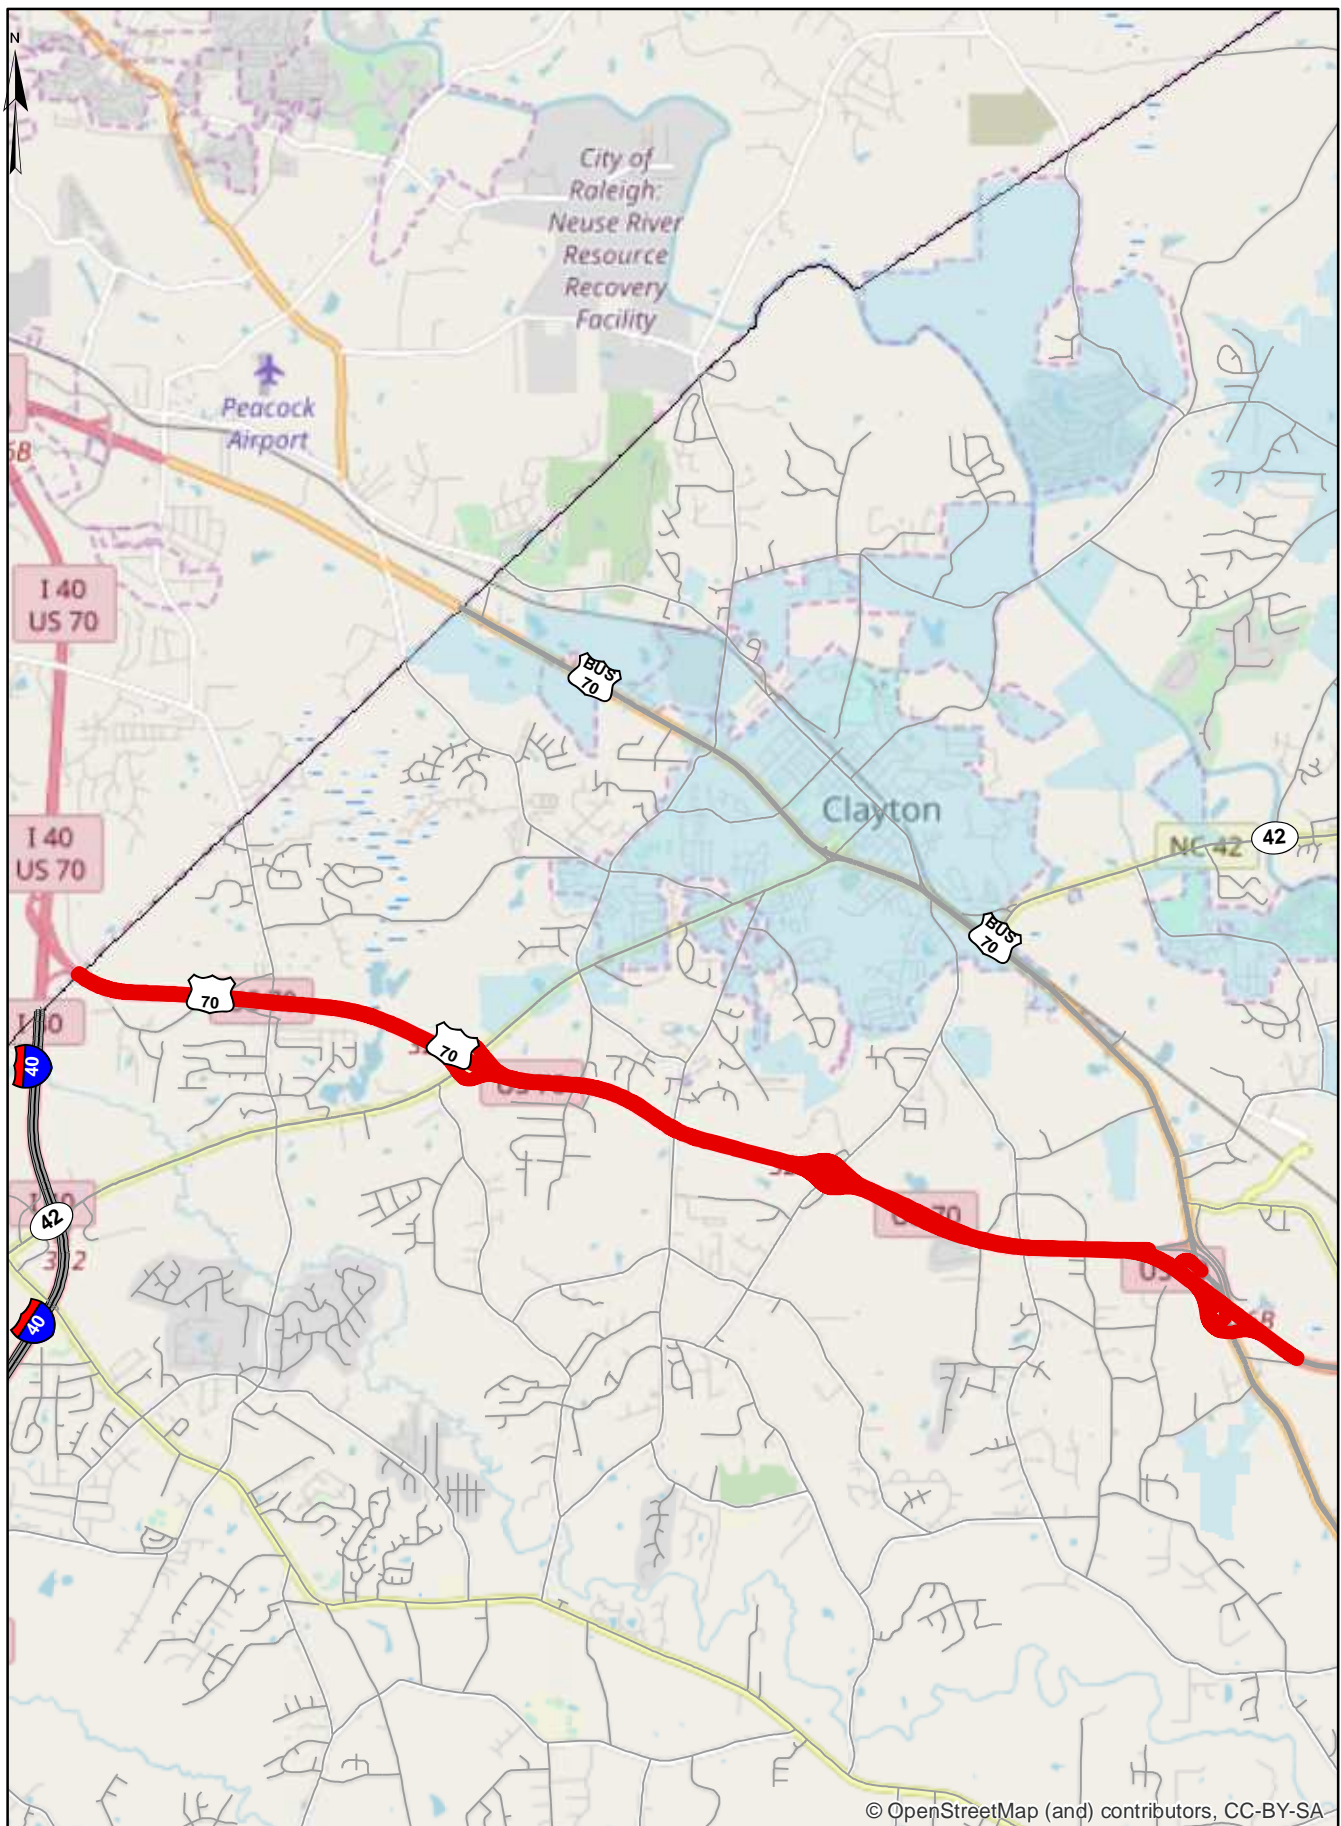

Resurface US 70 from Wake County Line to SR 2566 (Sadisco Road) - Completed October 2018

I-6044 - Interstate Maintenance US 70 Johnston County

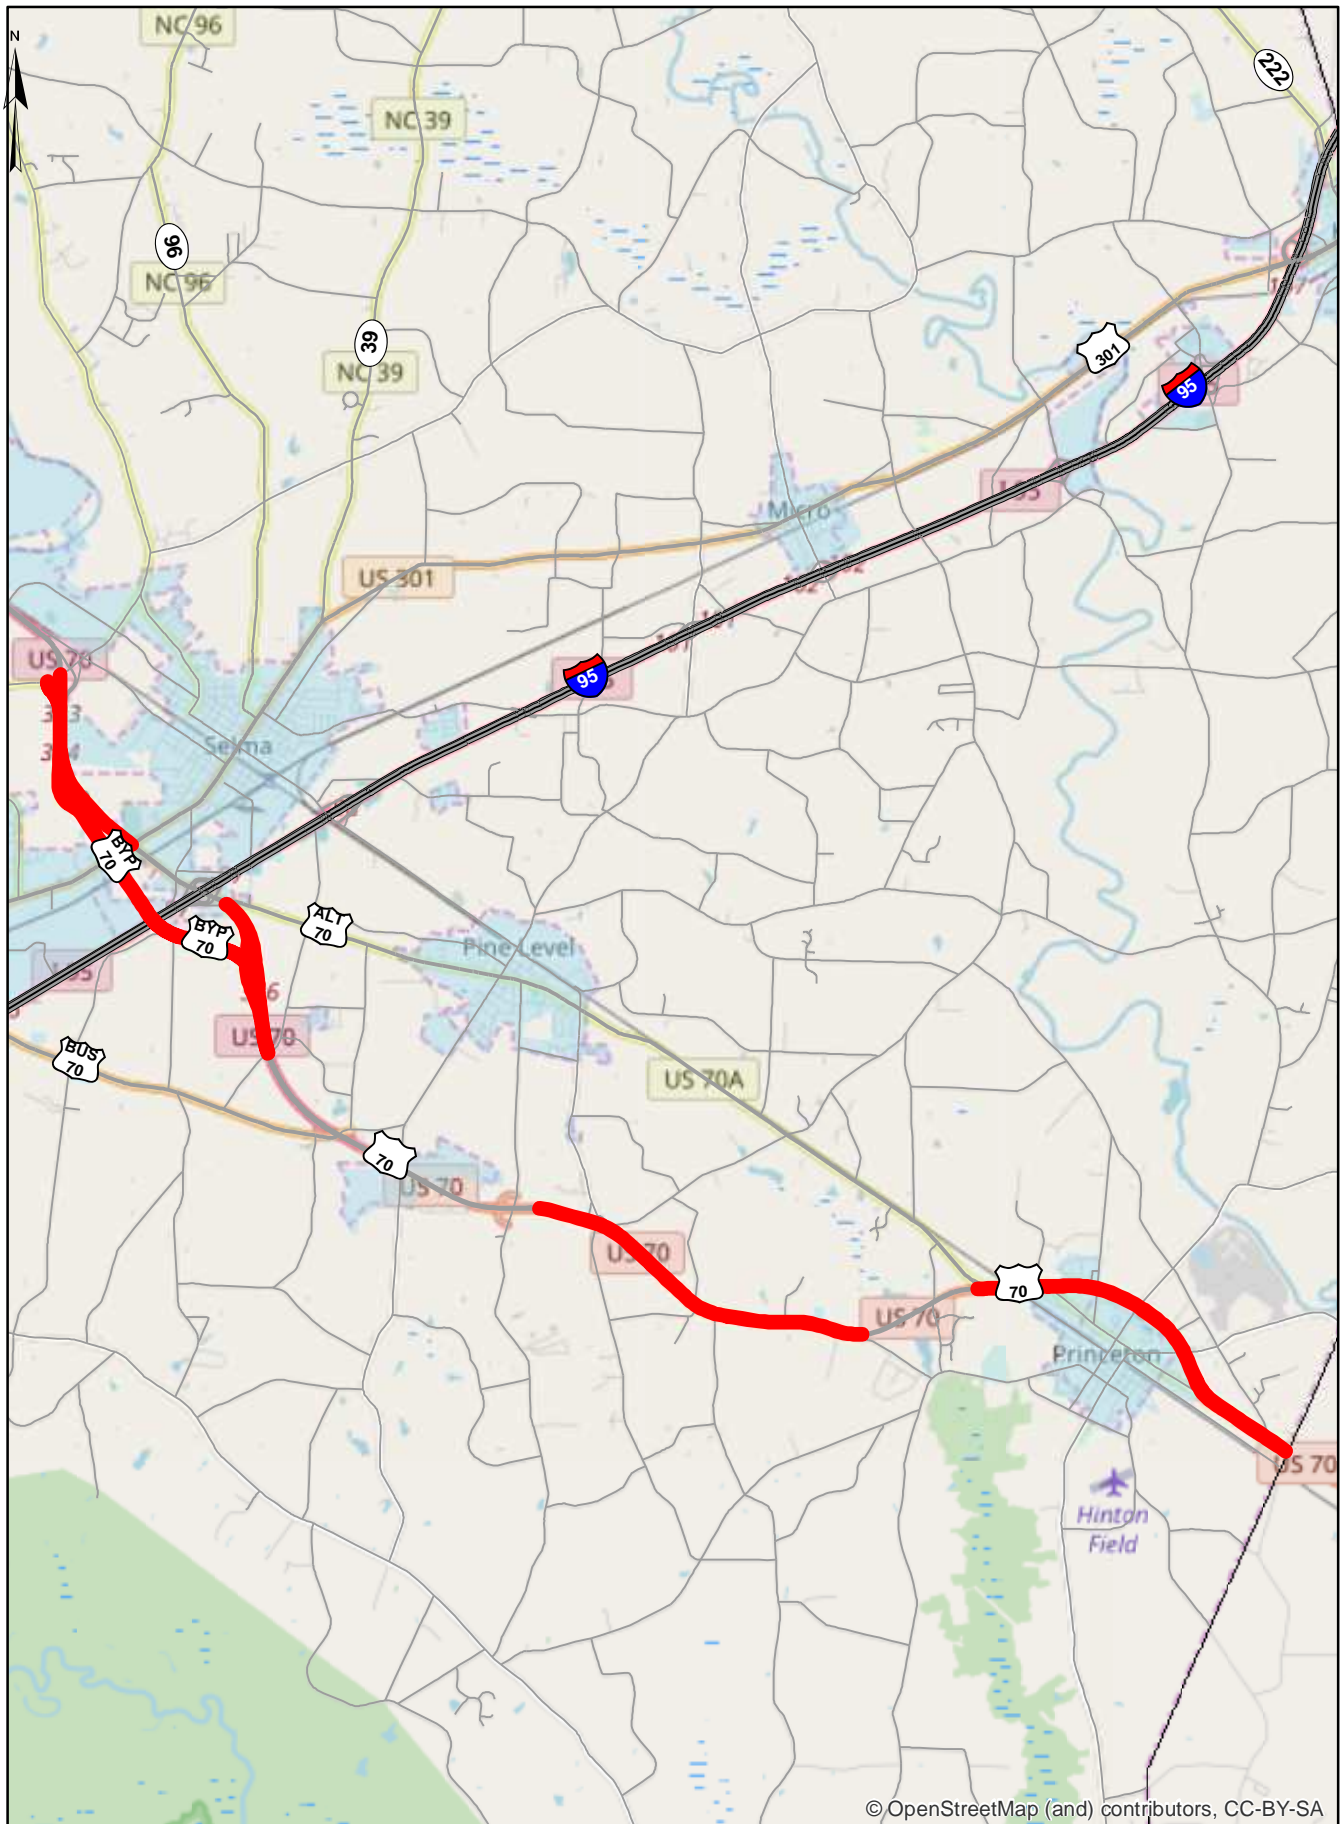

© OpenStreetMap (and) contributors, CC-BY-SA

Resurface, drainage structure repairs and guardrail updates (excluding previous projects)

Let Date: May 2019
