

# **US 70 Projects Update**

**November 15, 2018**




**NCDOT**

## **DIVISION 4**

**Corridor Upgrades  
Feasibility Studies  
Resurfacing**

# TIP: W-5600

## US 70 Johnston County

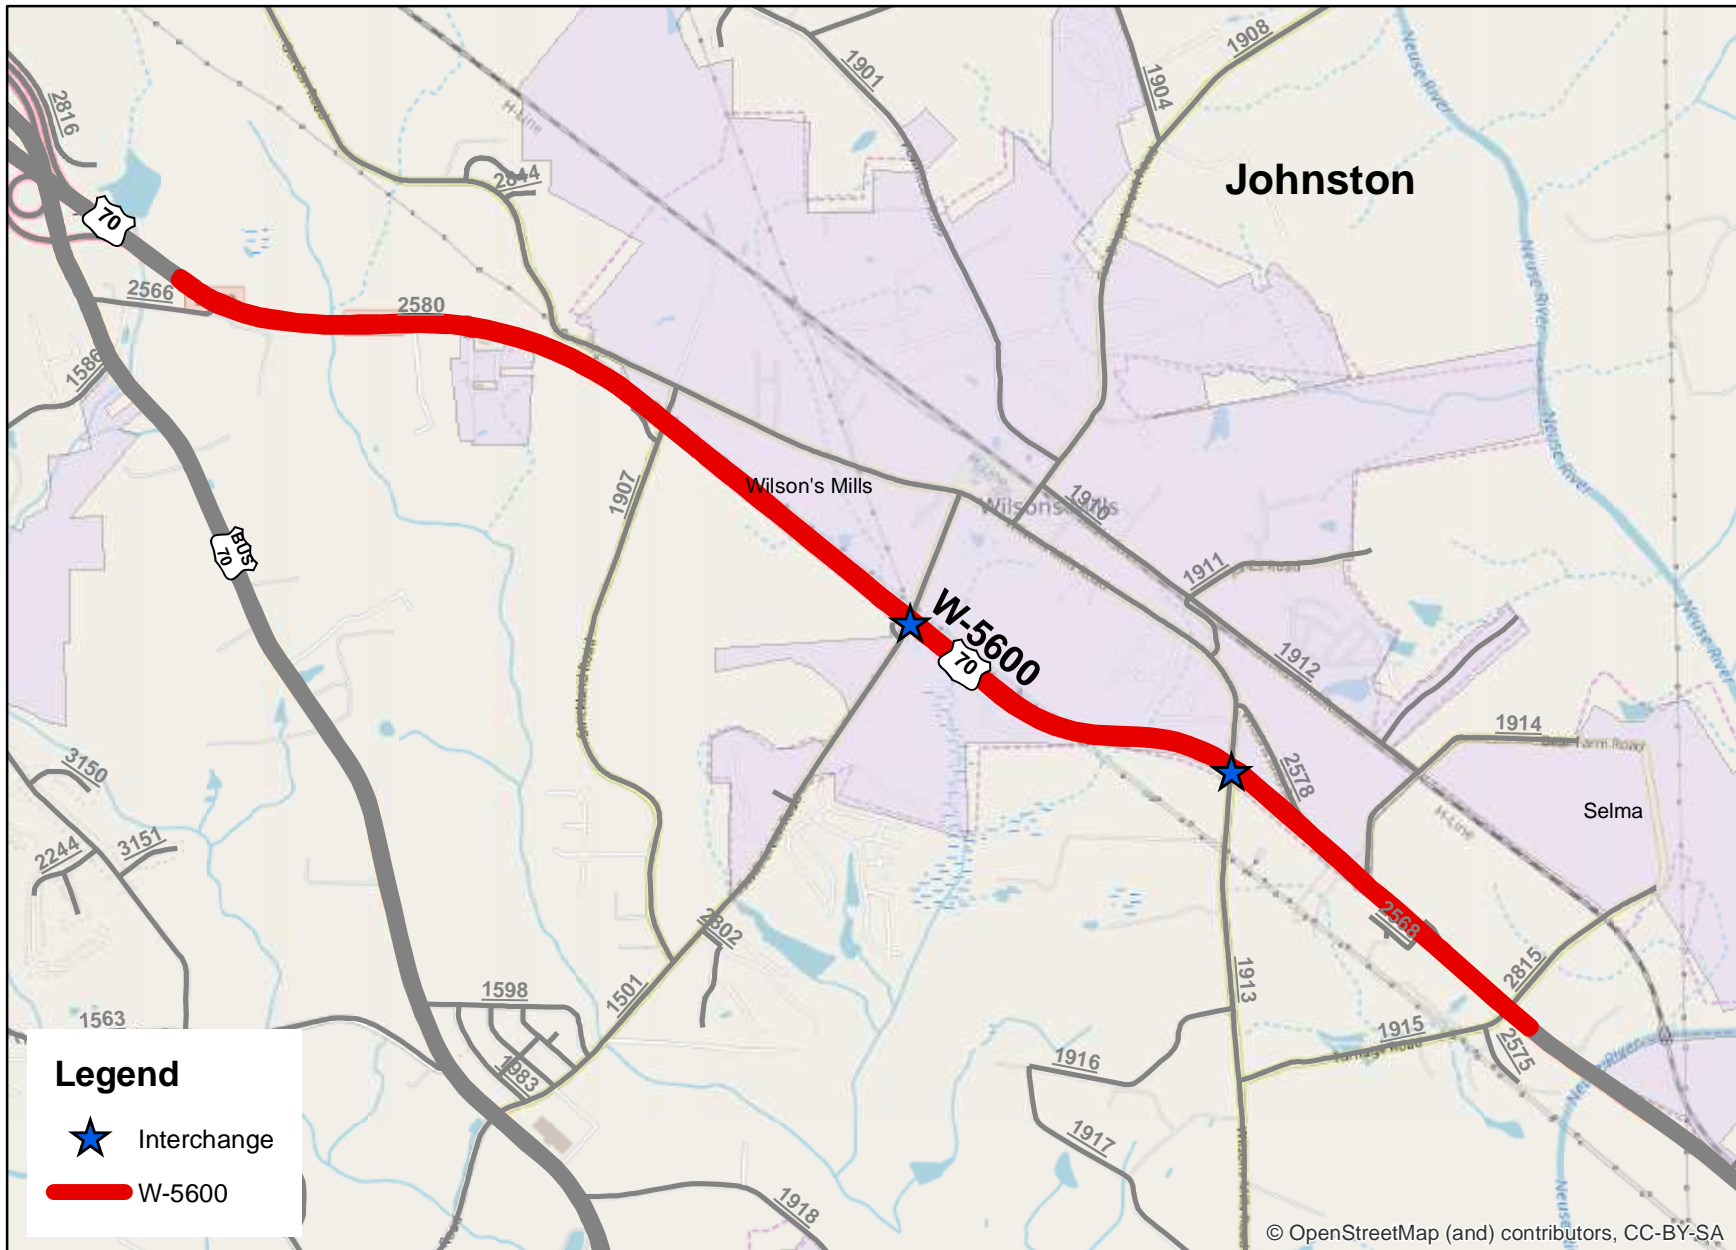

## **W-5600**

### **US 70 Improvements near Wilson's Mills - Johnston County**

#### **Project Description:**

Upgrade US 70 to Interstate standards from US 70 Business to Neuse River.

#### **Funding Status:**

Fully funded in 2018-2027 STIP.

#### **Schedule:**

- Project Scoping Meeting - July 2012
- Public Meeting - February 2016
- CE Approved - July 2016
- Right of Way Acquisition – March 2018
- Construction – Scheduled for September 2019

#### **Activities Underway**


- Right of way acquisition in progress.
- Utility design in progress.
- 90% plan preparation in progress.

#### **Upcoming Actions**

- Complete right of way acquisition.
- Complete utility designs and UBO plans.
- Utility relocations.
- 90% plan submittal.
- Pre-let field inspection.
- Final plans.
- Project letting and award.

Project Manager: Matt Clarke, P.E., (252) 640-6400, [wmclarke@ncdot.gov](mailto:wmclarke@ncdot.gov)

**TIP: R-5829**  
**US 70 Wayne - Johnston Counties**

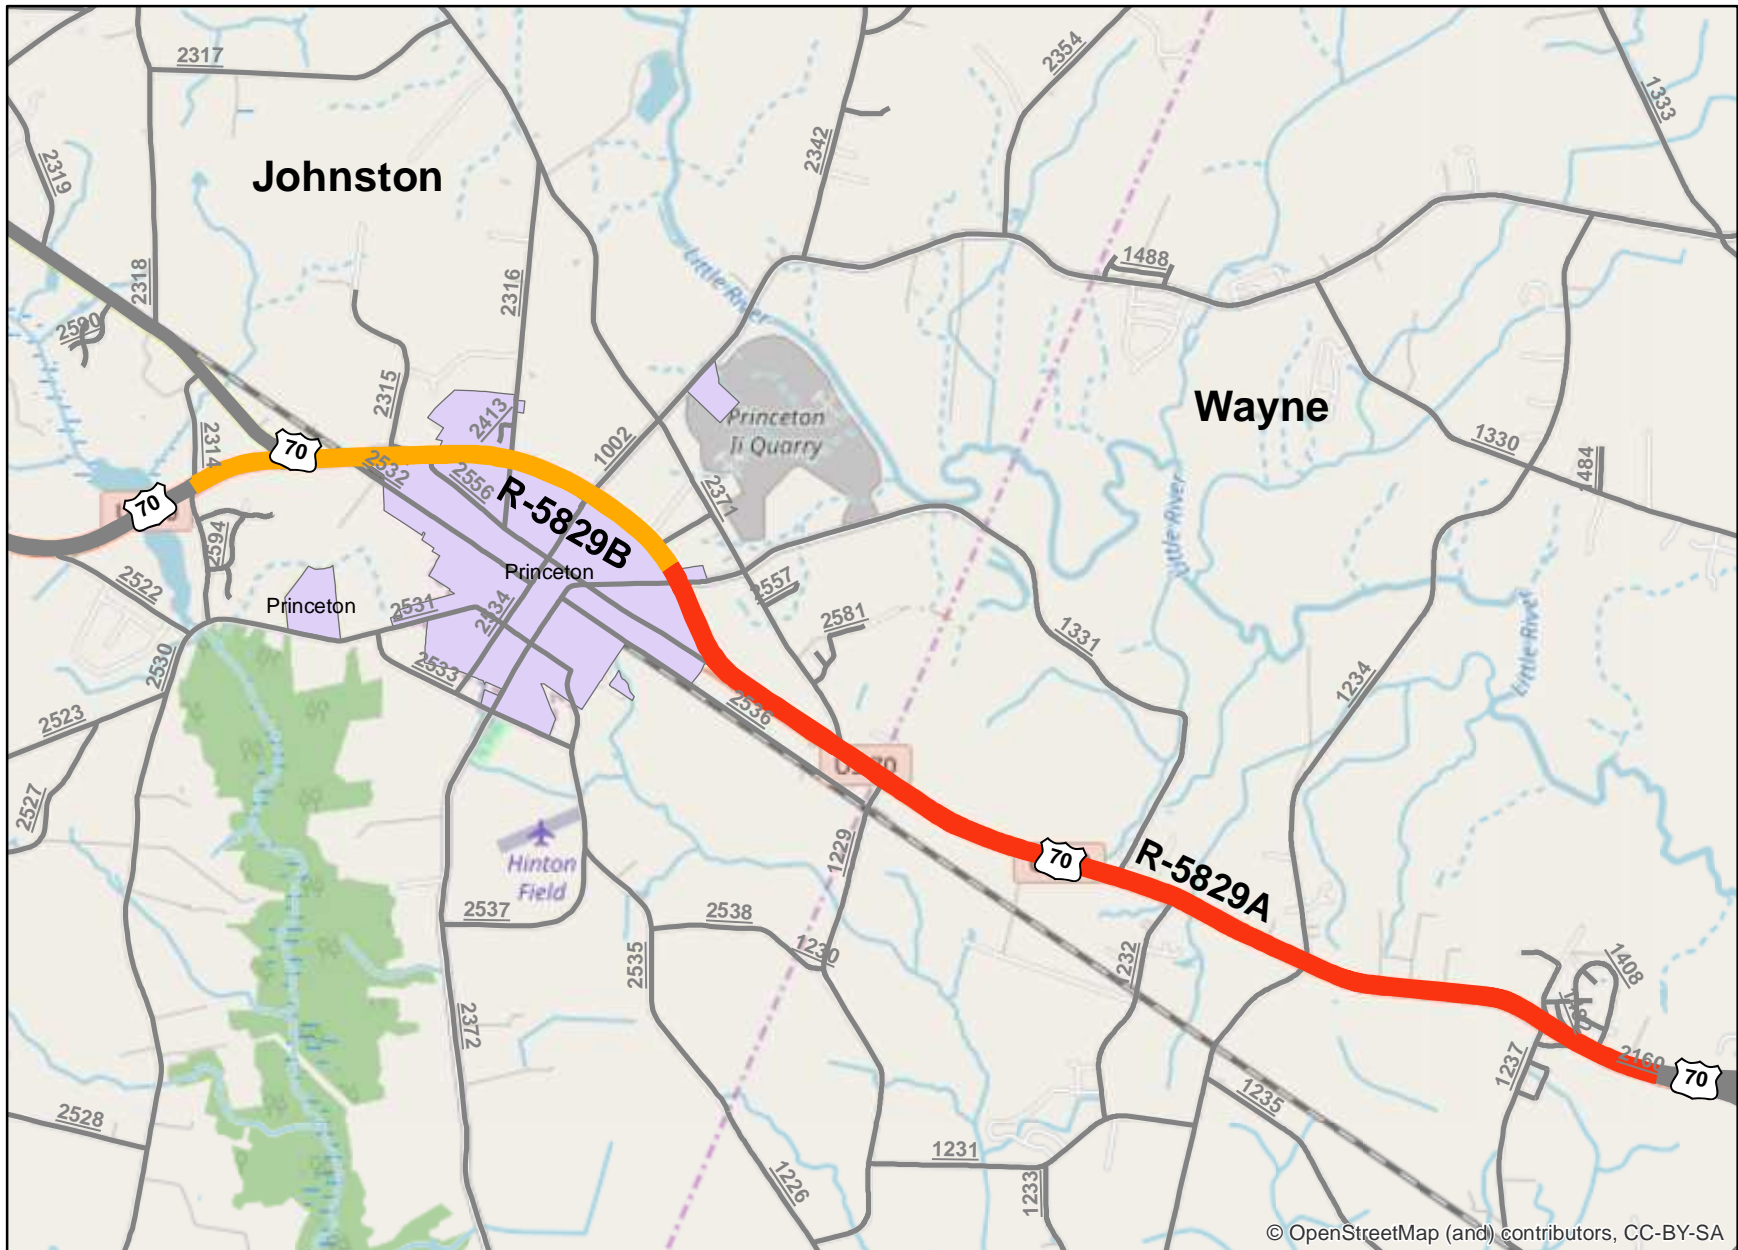

## **R-5829A & R-5829B**

### **US 70 Improvements near Princeton - Johnston County**

#### **Project Description:**

Upgrade US 70 to Interstate standards from US 70 Goldsboro Bypass to West of US 70A.

#### **Funding Status:**

Currently funded in 2018-2027 STIP.

#### **Schedule:**

- Traffic Forecast - May 2018
- Surveys Complete - December 2018
- Preferred Alternative Selected - October 2018
- Public Hearing - March 2019
- Environmental Document Approved - July 2019
- Design Build Let\* – R-5829A FY 2023

R-5829B FY 2027

#### **Activities Underway**

- Finalize Preliminary Design.
- Complete Environmental Assessment.
- Historic/Archaeology surveys.
- Noise Analysis.


#### **Upcoming Actions**

- Public Hearing
- Prepare for Design-Build Procurement.

Project Manager: Matt Clarke, P.E., (252) 640-6400, [wmclarke@ncdot.gov](mailto:wmclarke@ncdot.gov)


**\*Design Build Let may provide accelerated schedule**

# FS-1604A - US 70 Johnston County

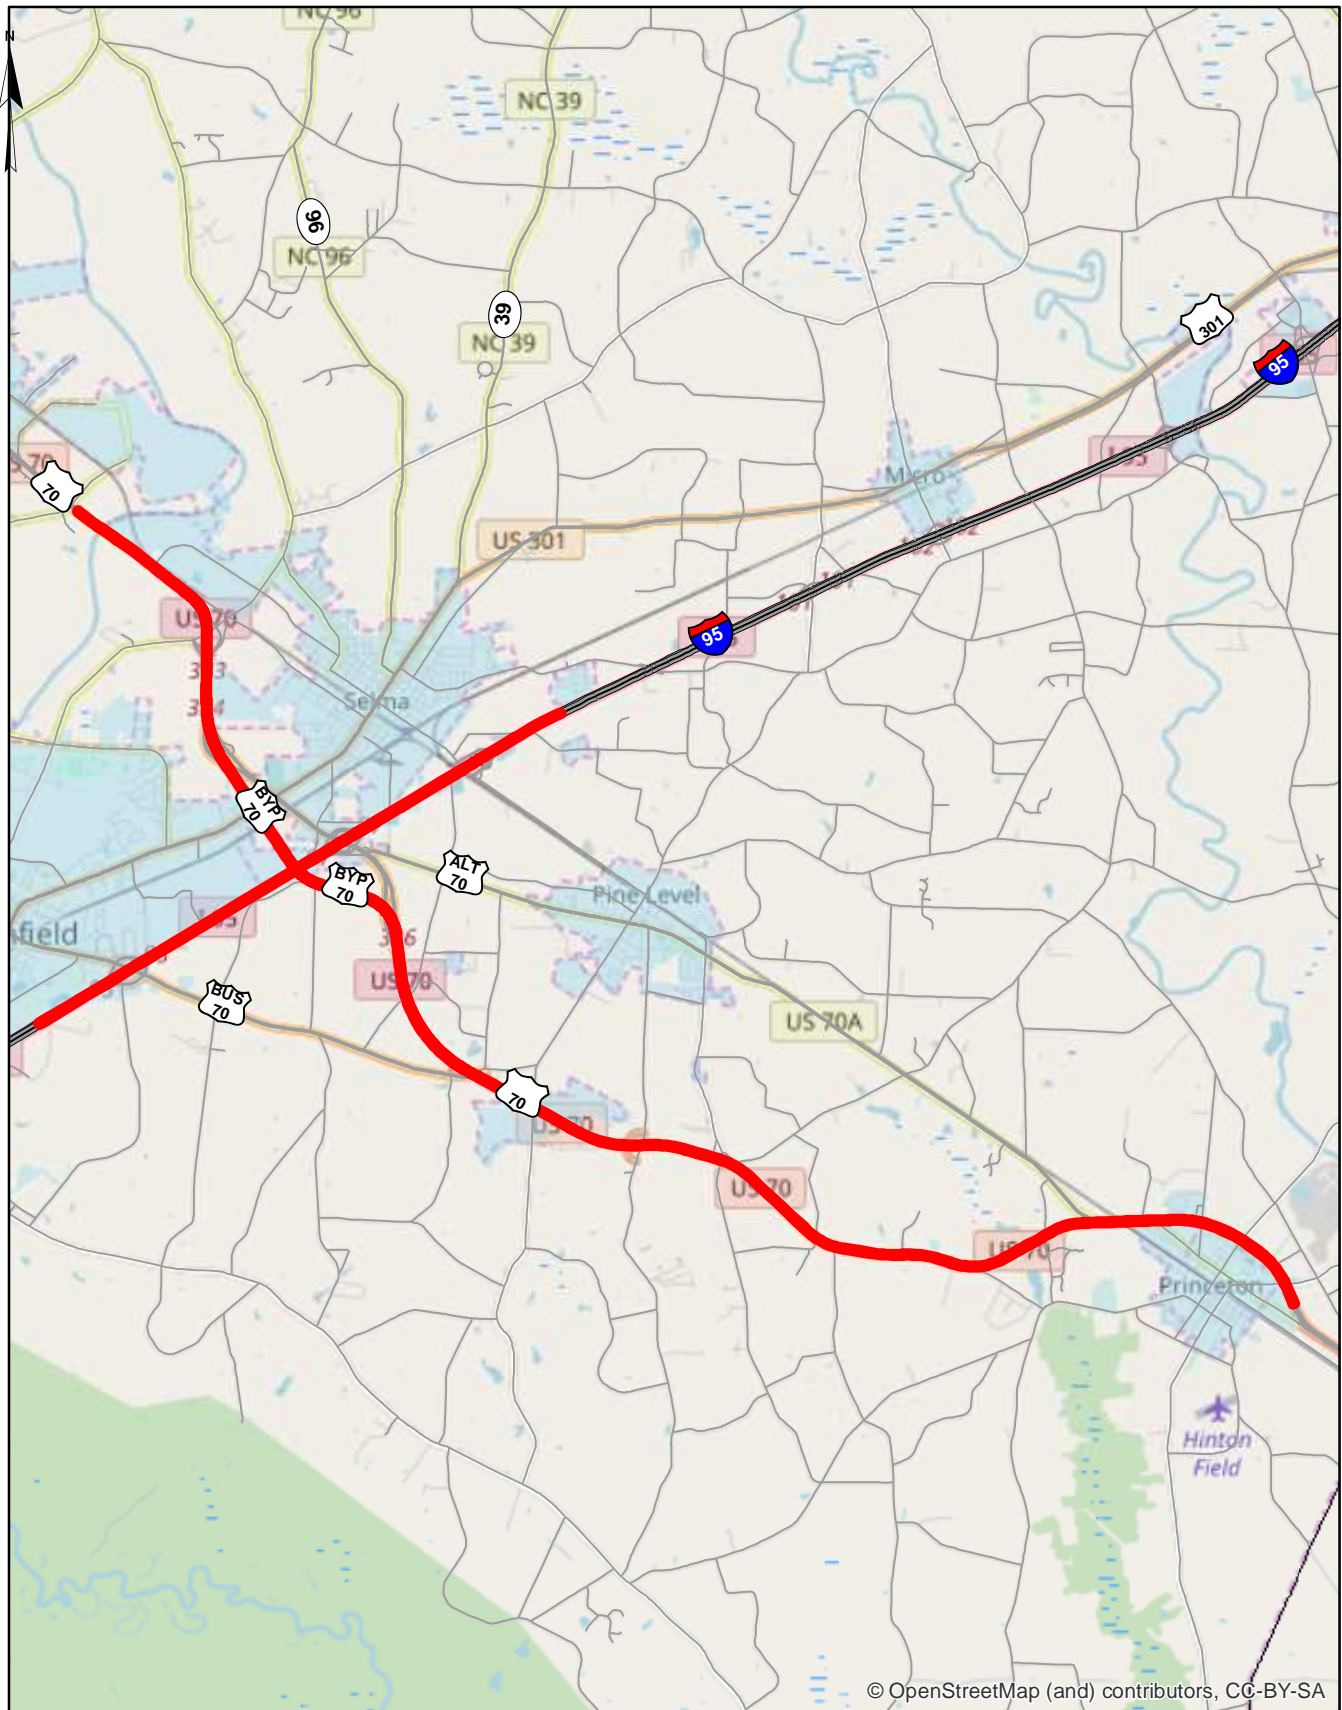


Feasibility Study for US 70 from SR 1003 (Buffalo Road) near Selma to SR 2372 (Edwards Road) in Princeton Completed Date: August 2018  
Link: [https://connect.ncdot.gov/projects/planning/FeasibilityStudiesDocuments/Feasibility-Study\\_1604A\\_Report\\_2018.pdf](https://connect.ncdot.gov/projects/planning/FeasibilityStudiesDocuments/Feasibility-Study_1604A_Report_2018.pdf)

# C204032 - US 70 Johnston County Resurfacing

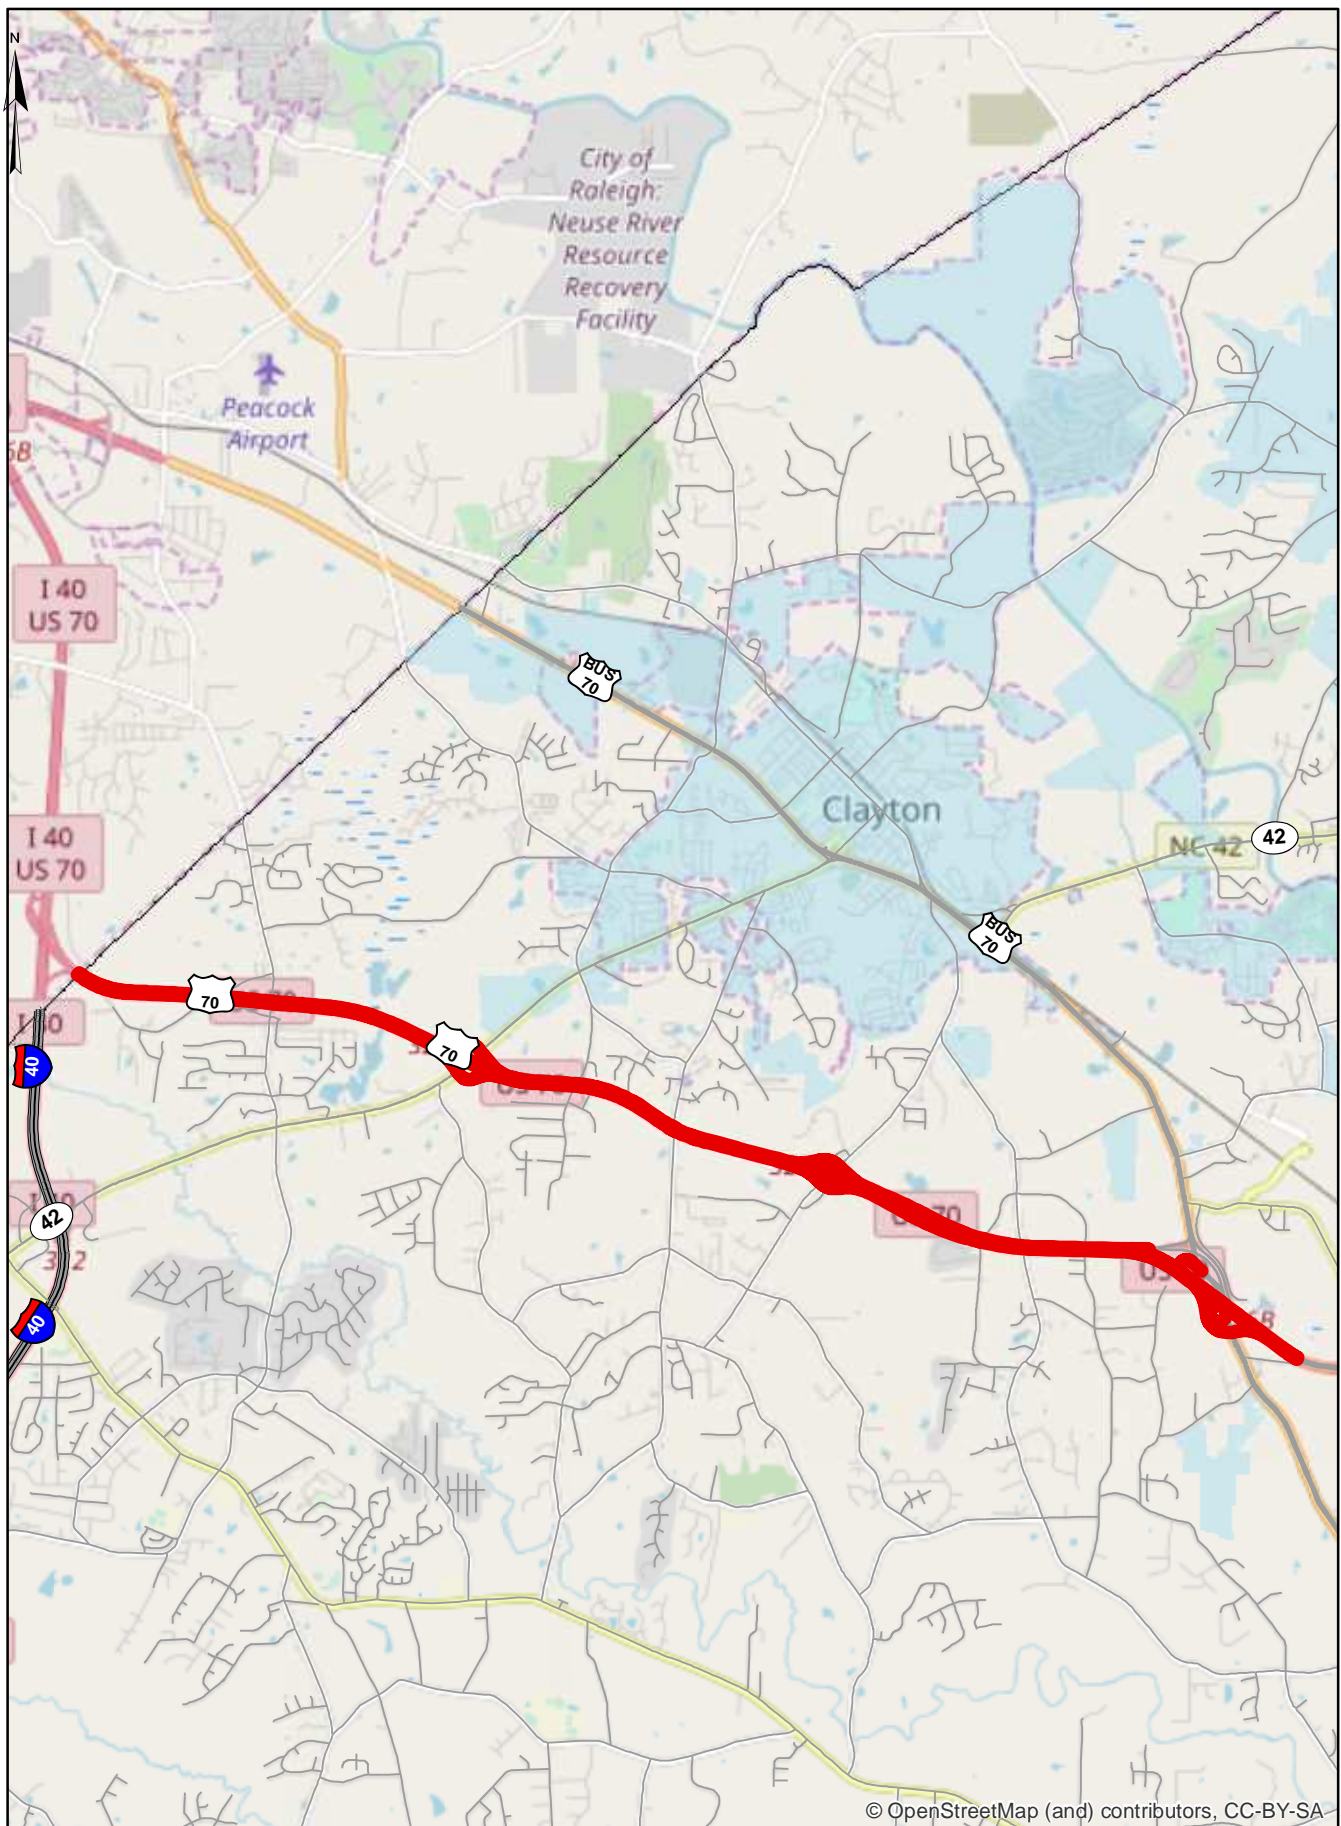

Resurface US 70 from Wake County Line to SR 2566 (Sadisco Road) - Completed October 2019

# I-6044 - Interstate Maintenance US 70 Johnston County

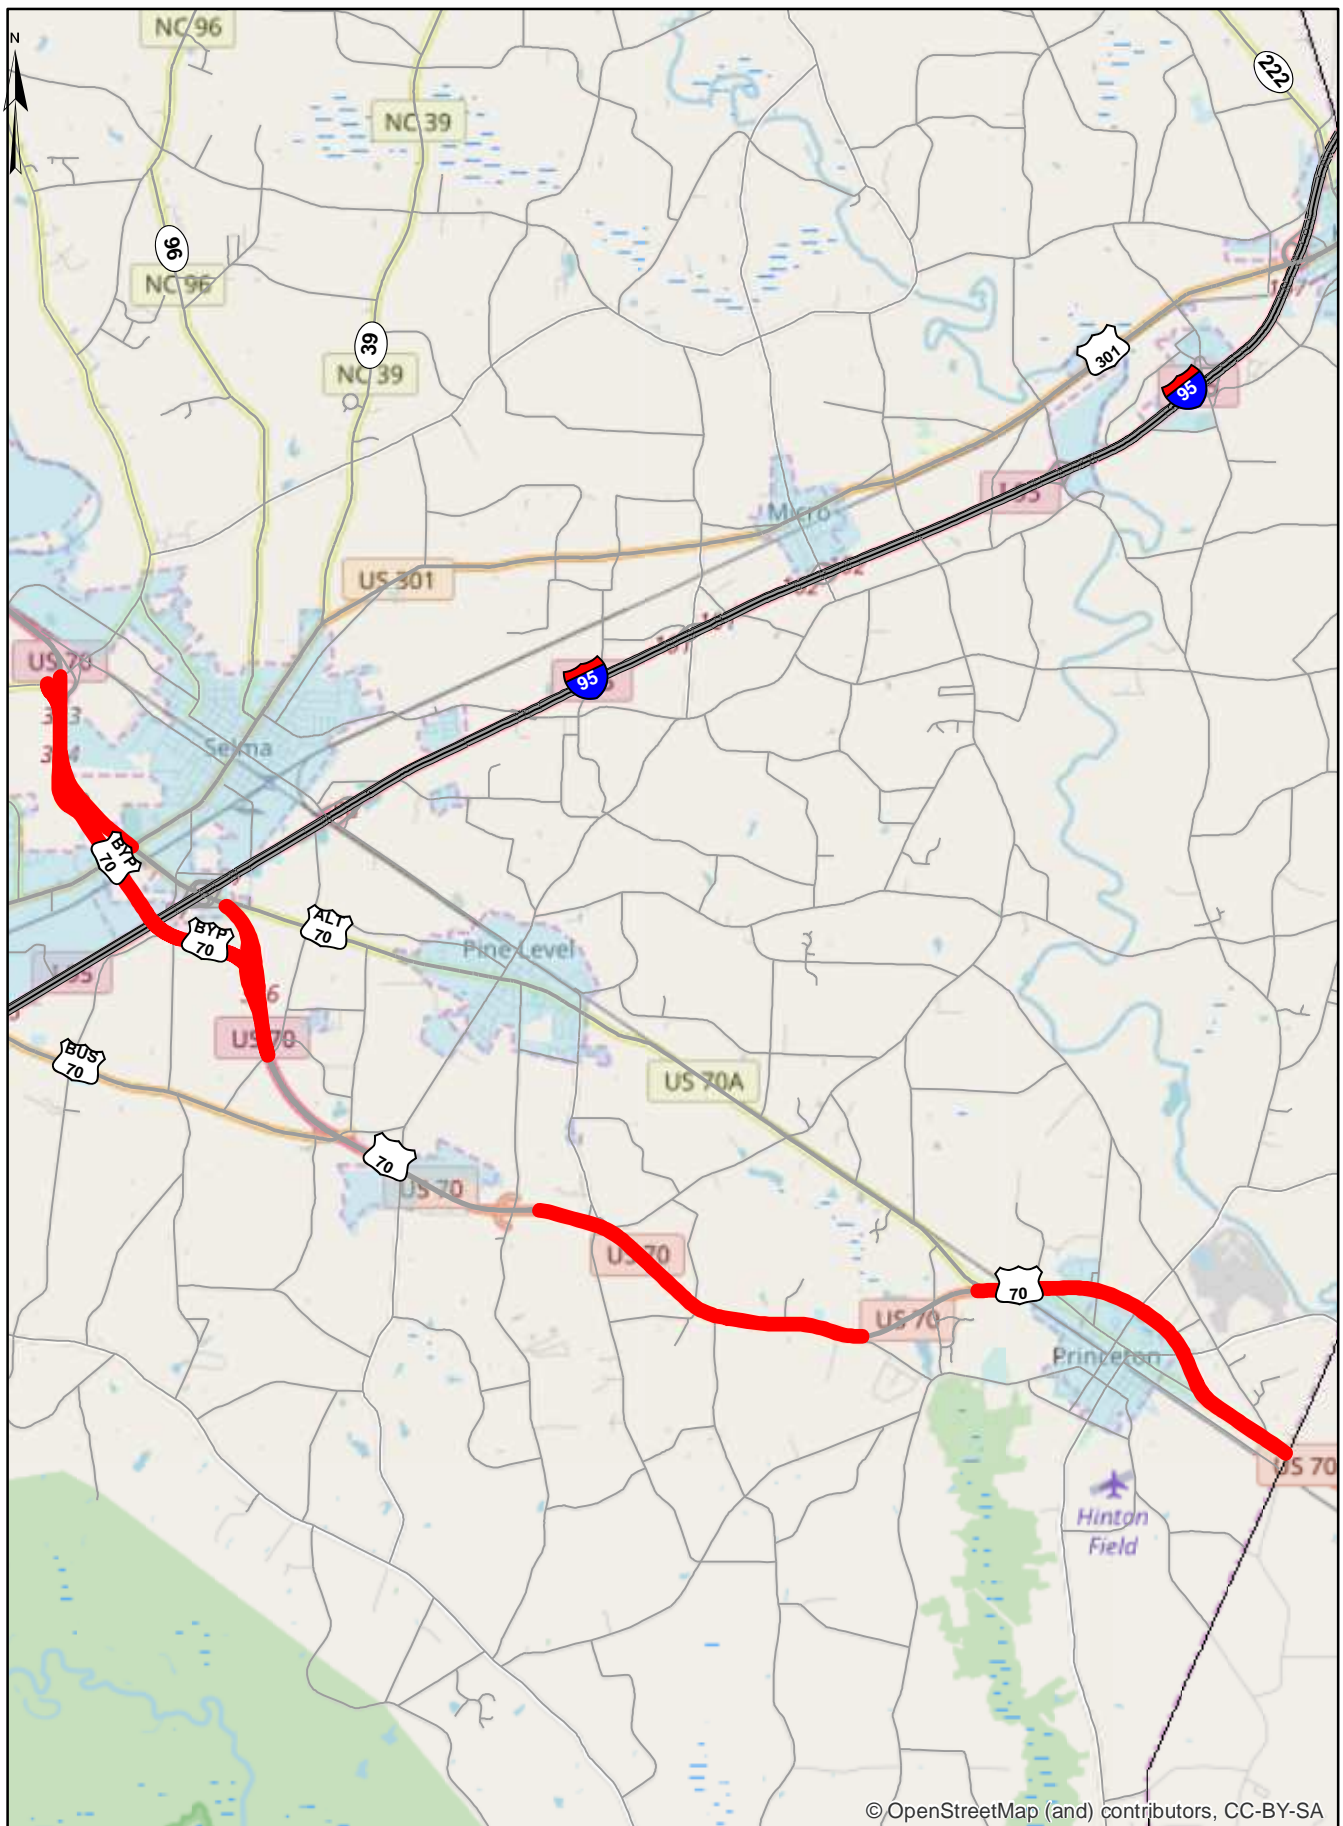

Resurface, drainage structure repairs and guardrail updates (excluding previous projects)  
Let Date: Spring 2019
