

# **NC Board of Transportation US 70 Workgroup**

**July 19, 2018**




**NCDOT**

**DIVISION 4**

**Corridor Upgrades  
Feasibility Studies  
Resurfacing**

# TIP: W-5600

## US 70 Johnston County

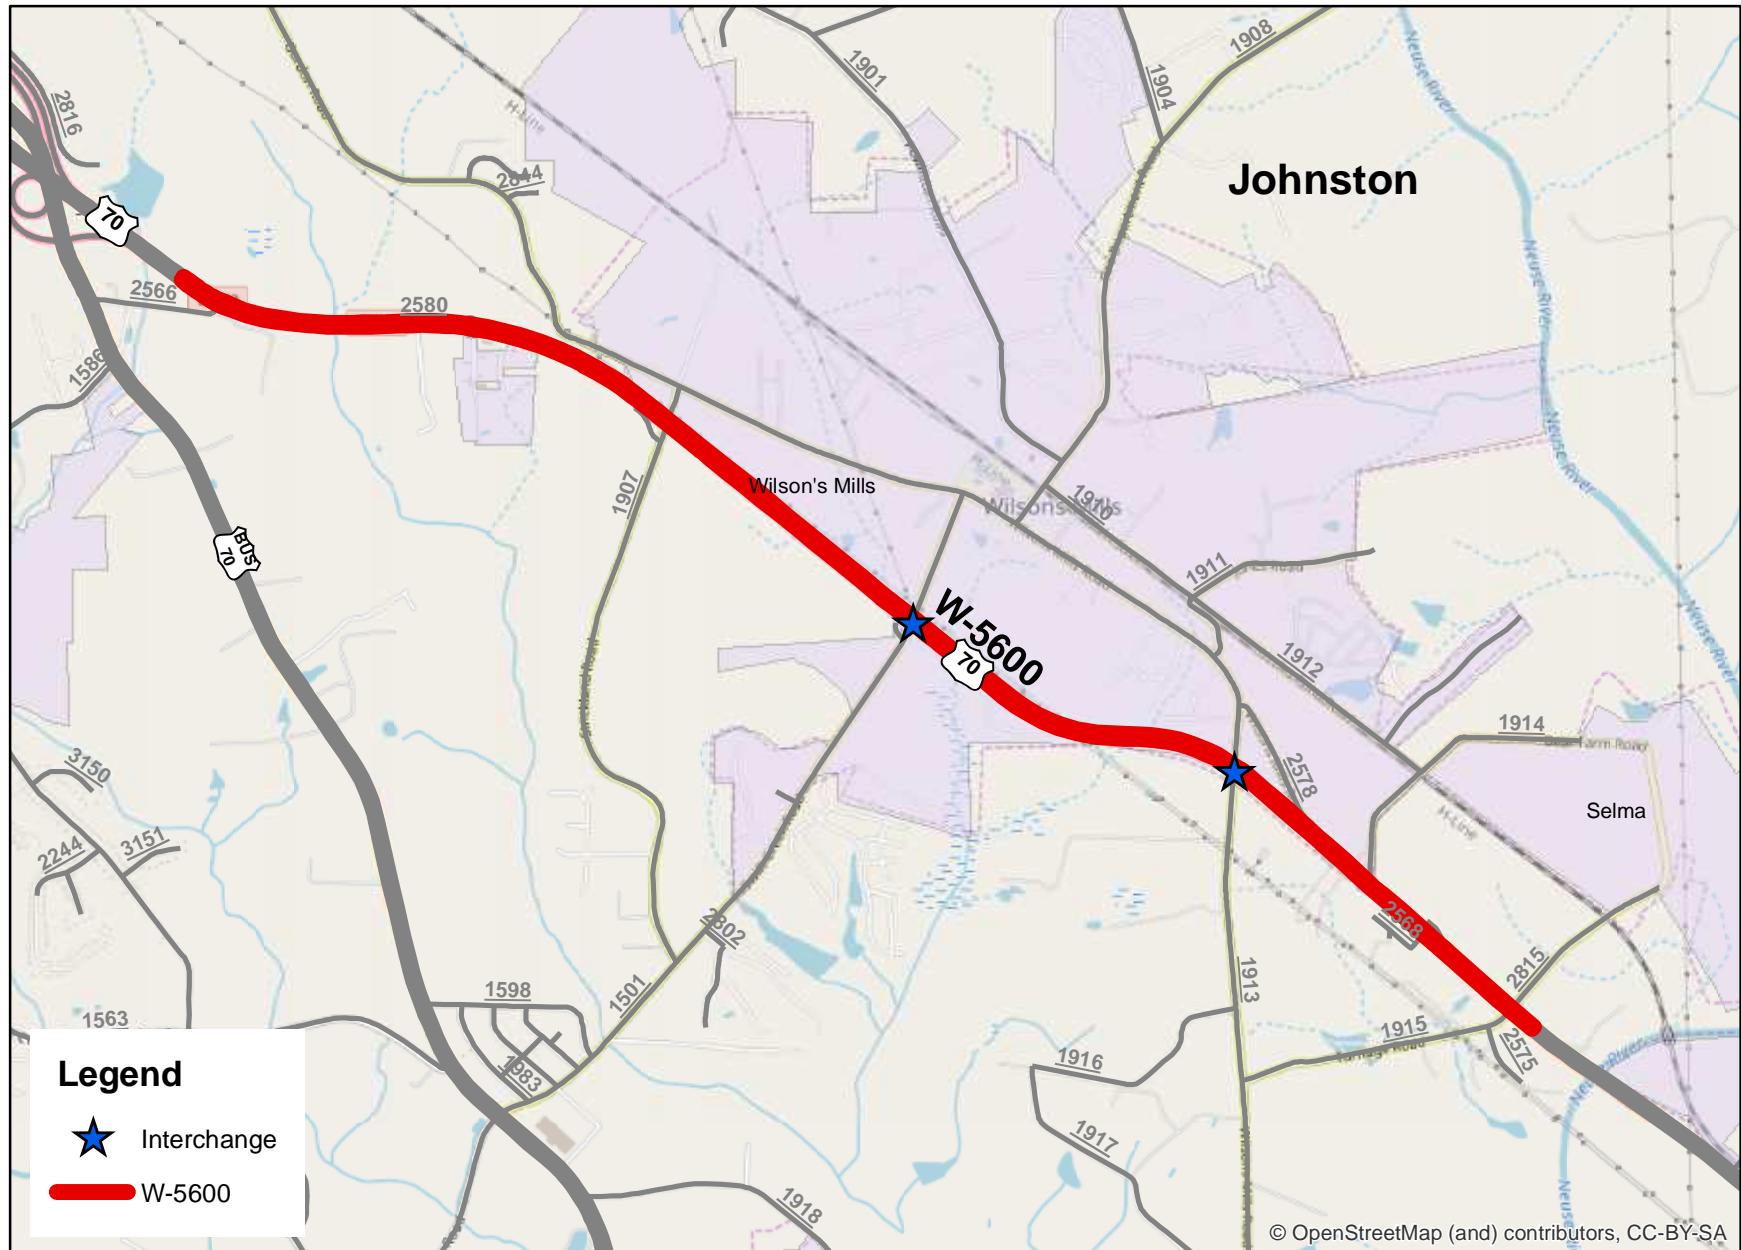

## **W-5600**

### **US 70 Improvements near Wilson's Mills - Johnston County**

#### **Project Description:**

Upgrade US 70 to Interstate standards from US 70 Business to Neuse River.

#### **Funding Status:**

Fully funded in 2018-2027 STIP.

#### **Schedule:**

- Project Scoping Meeting - July 2012
- Public Meeting - February 2016
- CE Approved - July 2016
- Right of Way Acquisition – March 2018
- Construction – Scheduled for September 2019

#### **Activities Underway**


- Right of way acquisition in progress.
- Utility design in progress.
- 90% plan preparation in progress.

#### **Upcoming Actions**

- Complete right of way acquisition.
- Complete utility designs and UBO plans.
- Utility relocations.
- 90% plan submittal.
- Pre-let field inspection.
- Final plans.
- Project letting and award.

Project Manager: Matt Clarke, P.E., (252) 640-6400, [wmclarke@ncdot.gov](mailto:wmclarke@ncdot.gov)

**TIP: R-5829**  
**US 70 Wayne - Johnston Counties**

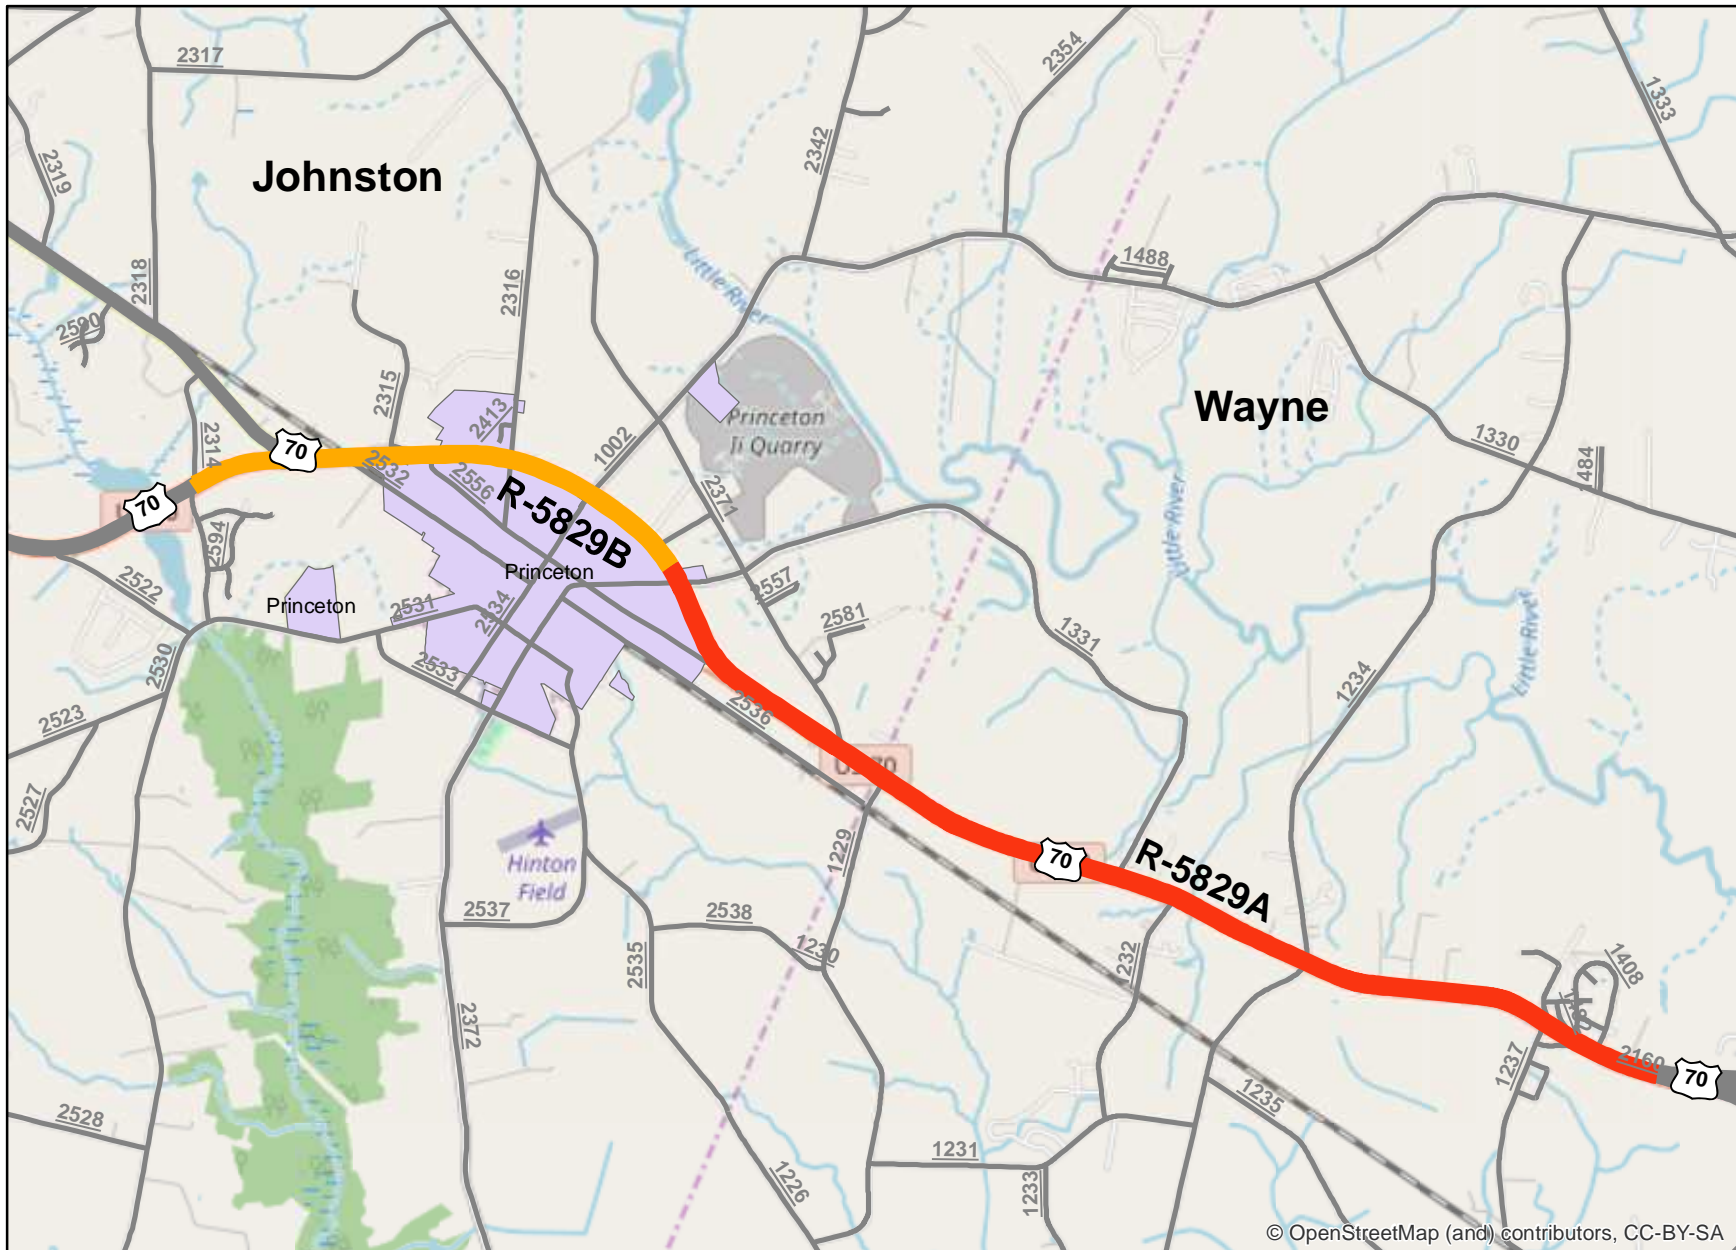

## **R-5829A & R-5829B**

### **US 70 Improvements near Princeton - Johnston County**

#### **Project Description:**

Upgrade US 70 to Interstate standards from US 70 Bypass to West of Luby Smith Road.

#### **Funding Status:**

Currently funded in 2018-2027 STIP.

#### **Schedule:**

- Traffic Forecast - May 2018
- Surveys Complete - August 2018
- Select Preferred Alternative - August 2018
- Public Hearing - March 2019
- Environmental Document Approved - July 2019
- 25% Plans Complete - August 2019
- Design Build Let\* – R-5829A FY 2023  
R-5829B FY 2027

#### **Activities Underway**

- Functional design of alternatives.
- Environmental assessment of alternatives.
- Historic/Archaeology surveys.

#### **Upcoming Actions**


- Preferred alternate selection.
- Begin 25% design.

Project Manager: Matt Clarke, P.E., (252) 640-6400, [wmclarke@ncdot.gov](mailto:wmclarke@ncdot.gov)

**\*Design Build Let may provide accelerated schedule**



# FS-1604A - US 70 Johnston County DRAFT

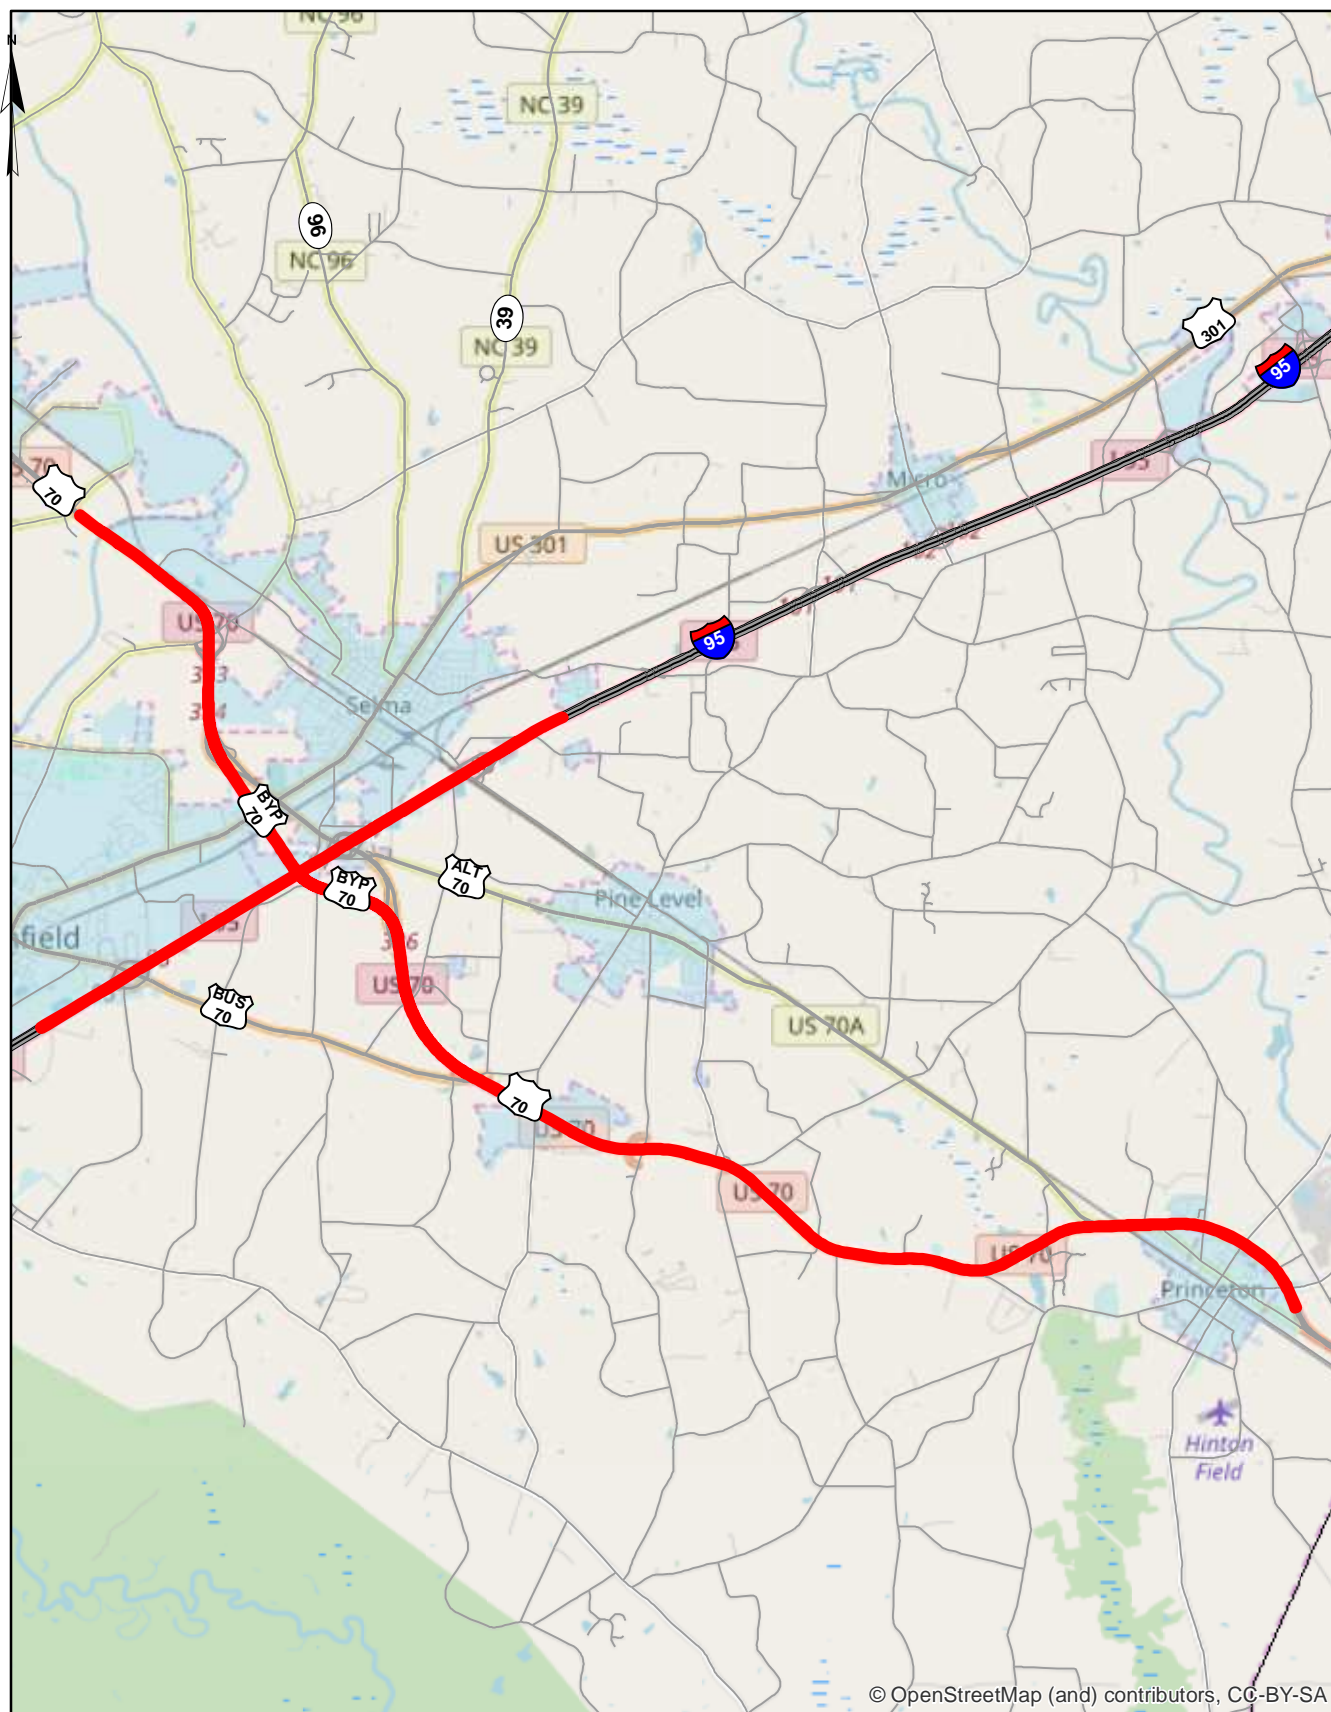

DRAFT


Feasibility Study for US 70 from SR 1003 (Buffalo Road) near Selma to SR 2372 (Edwards Road) in Princeton

Public Comment Period ends July 20, 2018

Completion Date: September 2018

Link: [www.ucprpo.org/Documents/feasibility/FS-1604A US 70 Feasibility Study FINAL DRAFT May 2018.pdf](http://www.ucprpo.org/Documents/feasibility/FS-1604A%20US%2070%20Feasibility%20Study%20FINAL%20DRAFT%20May%202018.pdf)


# C204032 - US 70 Johnston County Resurfacing

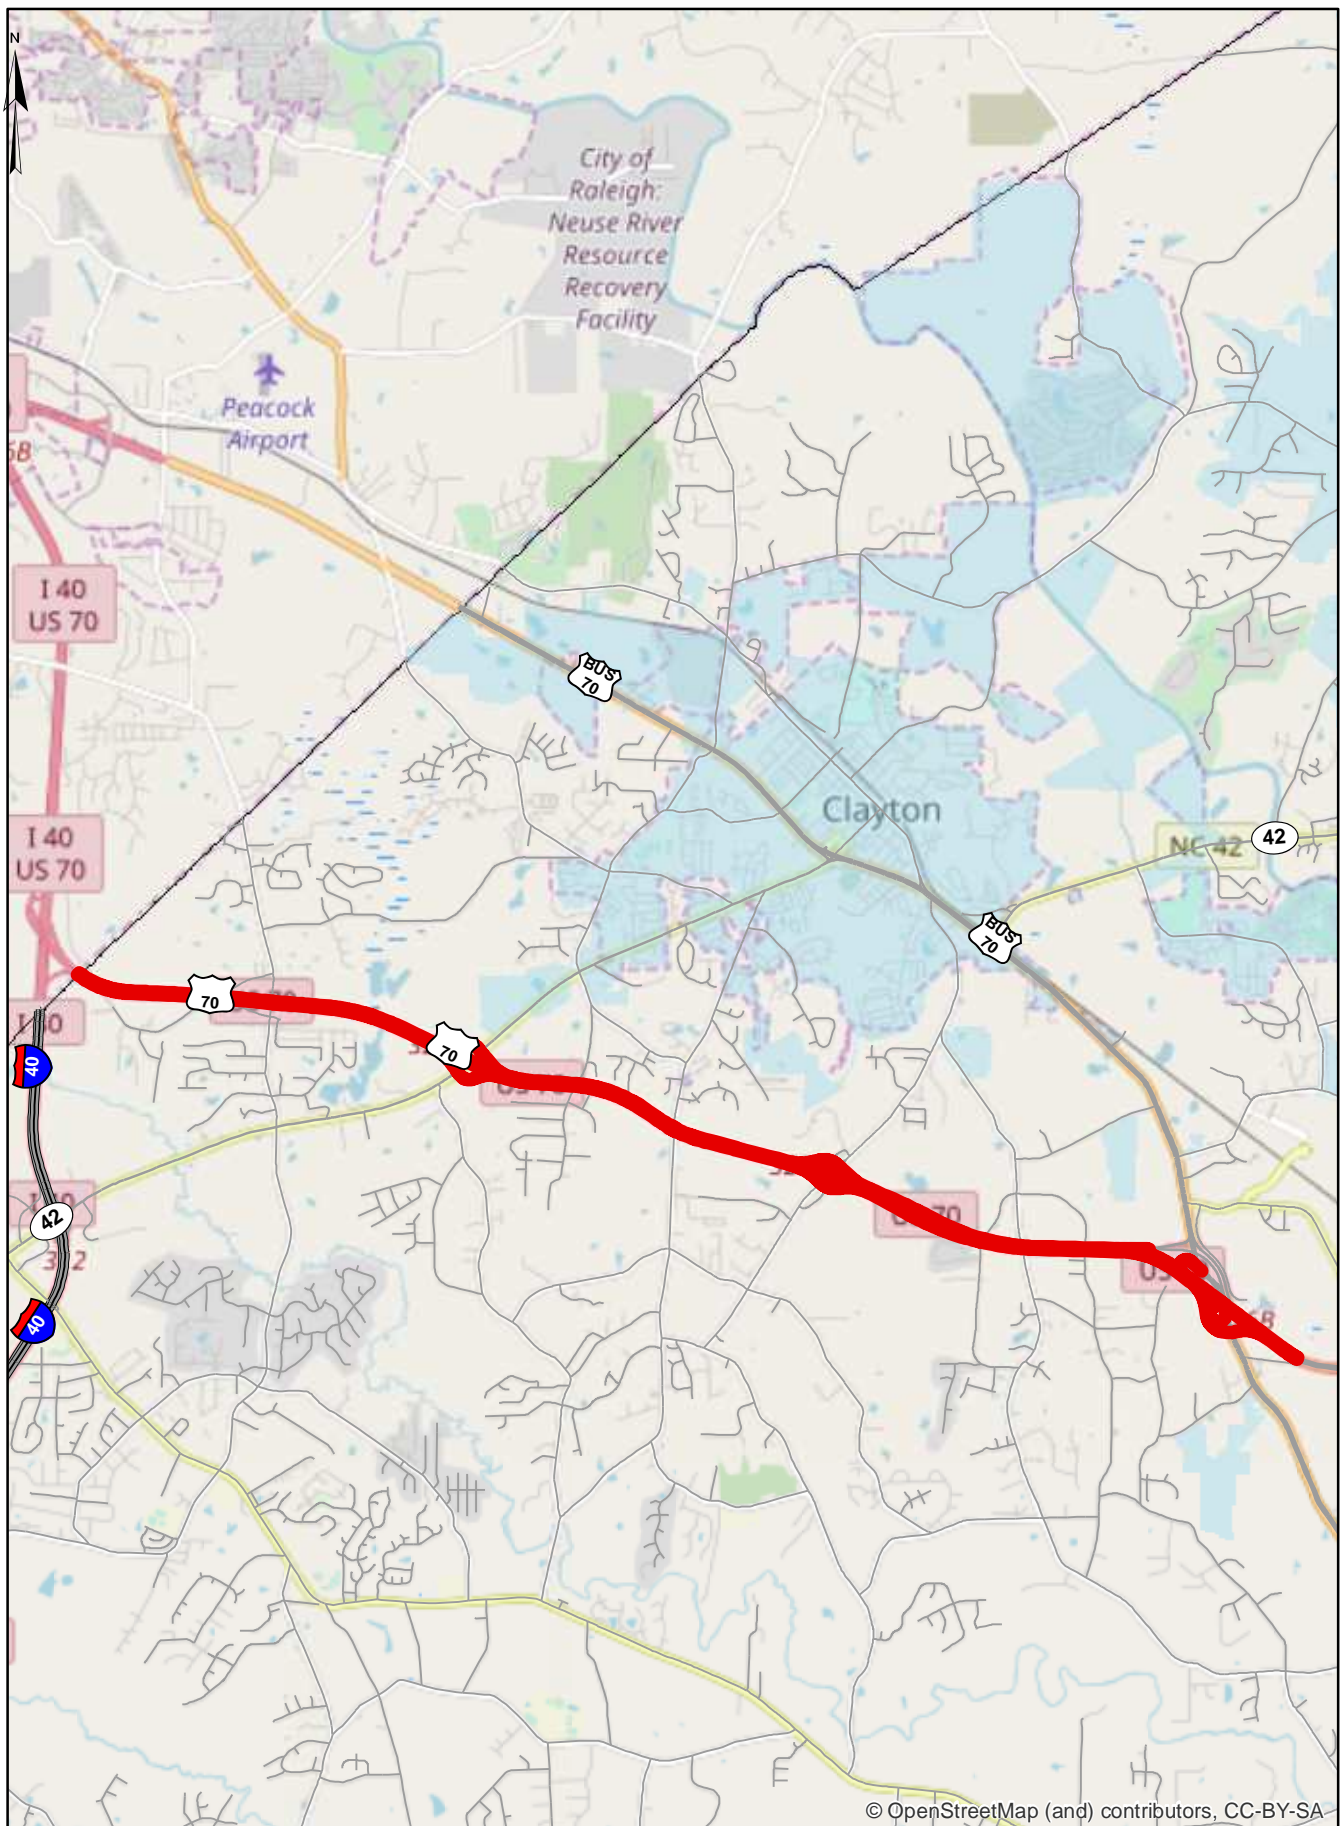

Resurface US 70 from Wake County Line to SR 2566 (Sadisco Road) - 90% Complete  
Contract Completion Date: October 19, 2018



# I-6044 - Interstate Maintenance US 70 Johnston County

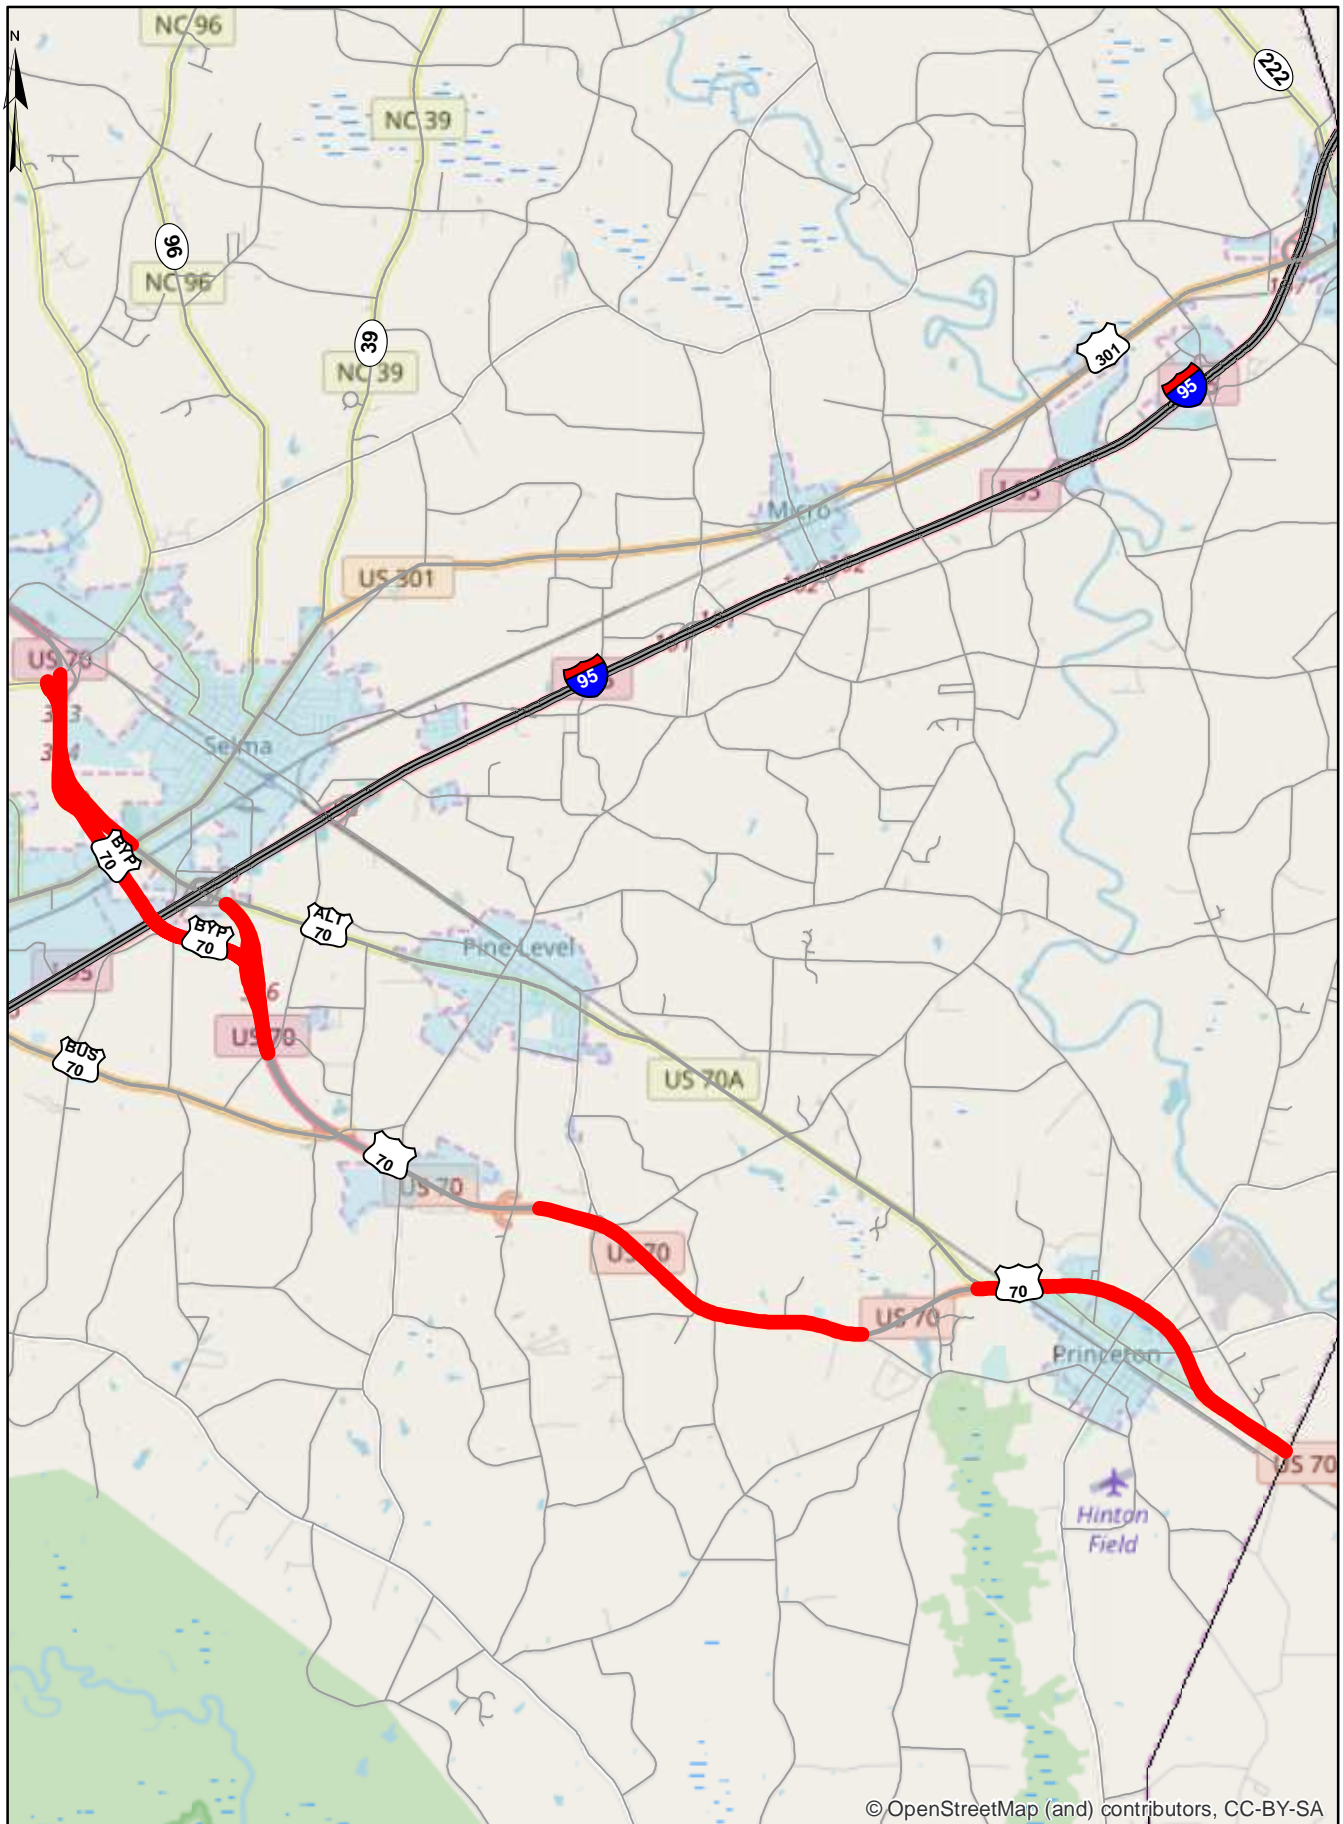

© OpenStreetMap (and) contributors, CC-BY-SA

Resurface, drainage structure repairs and guardrail updates (excluding previous projects)  
Let Date: Spring 2019
